AIPMS Proposal - Addressing Infrastructure Programme Management System

RFP Reference: AIPMS-RFP-001 v2.0 **Issue Date:** 10 March 2026 **Submitted to:** Inspired Global Systems Ltd (IGSL)
Submitted by: Inspired Delta Ltd

Table of Contents

1. Section A: Executive Summary
2. Section B: Respondent Profile & Credentials
3. Section C: Technical Approach
4. Section D: Project Plan & Delivery Timeline
5. Post-Installation Support Model
6. Section E: Commercial Proposal
7. Section F: Compliance Declarations
8. Submission Checklist for Final PDF

Section A: Executive Summary

Inspired Delta Ltd submits this proposal for the supply, configuration, hosting, and support of the Addressing Infrastructure Programme Management System (AIPMS). Our recommended delivery model is a hybrid implementation built on ERPNext and the Frappe Framework, with targeted custom modules for the AIPMS Configuration Panel, Field Data Tool (FDT) integration, programme-specific workflows, and reporting requirements.

The solution is designed to meet the RFP objective of delivering a rapid, operational programme platform without taking on the cost and schedule risk of a full bespoke build. We will use proven ERPNext capabilities for contracts, HR, payroll, document management, workflow, dashboards, and auditability, then extend them where the RFP requires programme-specific controls such as selective vendor workflows, payment certification logic, field-level HR restrictions, and FDT import validation.

Lite Version for Modules 1-5 by end of Week 2, ahead of the Week 3 hard deadline.

ERPNext/Frappe foundation with open exports, transparent configuration, and continuity beyond a single vendor.

Configuration-driven financial parameters, RBAC, audit trail, document control, and payment workflow governance.

Proposal statements required by the RFP:

- Inspired Delta Ltd confirms that it has reviewed the AIPMS RFP in full and will complete the detailed Annex A compliance matrix as part of the final submission package.
- Inspired Delta Ltd accepts the delivery timetable in Section 6 of the RFP, including the Week 3 Lite Version hard deadline and the Week 10 Full Go-Live hard deadline.
- Inspired Delta Ltd commits to an accelerated delivery target of **Lite Version by end of Week 2** and **Full Go-Live by end of Week 8**, subject to timely availability of programme parameters, approvers, and FDT sample data during mobilisation.

Section B: Respondent Profile & Credentials

Company Details

Company Name	Inspired Delta Ltd
Primary Email	info@ideltatech.com
Website	ideltatech.com
Registered Address	[Insert registered office address before final submission]
Registration No.	[Insert CAC registration number before final submission]
Primary Contact	[Insert bid contact name, title, phone, and email]

Respondent Profile

Inspired Delta Ltd delivers digital platforms, workflow automation, ERP implementations, and custom business systems using the Frappe/ERPNext stack. Our delivery approach combines configuration-led deployment with focused custom engineering where governance, reporting, integration, or data-control requirements demand it.

For AIPMS, we will deploy a delivery team spanning project management, solution architecture, Frappe development, QA, hosting, and HR/payroll configuration. This approach aligns directly with the RFP emphasis on rapid mobilisation, operational controls, data protection, and a 12-month support model post go-live.

B.1 Relevant Project Credentials

Reference Project	Comparable Scope	Relevance to AIPMS	Submission Note
Ingentia Energies	Programme controls, workflow approvals, reporting, and operational administration	Relevant for approval workflows, operational visibility, and programme-level reporting	Insert contract value, go-live date, and verification contact in final PDF appendix
One School Initiative	HR/payroll automation, staff data handling, attendance, and reporting	Relevant for AIPMS Module 7 payroll, onboarding, statutory deductions, and HR reporting	Insert contract value, go-live date, and verification contact in final PDF appendix
Infrastructure ERP deployment	Contract administration, procurement controls, document handling, and finance integration	Relevant for Modules 2, 3, and 4 controls and commercial governance	Replace with named client reference and full verification details before submission

Local Delivery Capacity

Inspired Delta Ltd will deliver AIPMS with a Nigeria-based implementation team, enabling rapid mobilisation, direct stakeholder engagement during Weeks 1-3, and local support during hypercare and Year 1 support retainer.

Data Protection Capability

The solution will be delivered under a controller-processor model with data access restricted by role and field, audit logging enabled, and HR/payroll records protected by explicit privilege boundaries. The final submission will include the applicable data protection statement and DPA commitment for the deployment jurisdiction.

Section C: Technical Approach

Section 7 Proposal Requirement Coverage

This section is structured to respond directly to the RFP proposal requirements for technical submission. Inspired Delta Ltd therefore addresses: the proposed platform and implementation model; module-by-module compliance against the seven AIPMS-FRS-001 v2.0 modules; the Configuration Panel approach; the HR module approach; the FDT integration approach; hosting, infrastructure, security, backup, and recovery; and the offline or low-connectivity operating model required for designated field activities.

Section 7 Requirement	Response in this Proposal
Proposed platform approach with justification	Covered under **Proposed Delivery Model** and **Why ERPNext Enables a Lite Version by Week 2**, setting out the hybrid ERPNext/Frappe approach and the justification for a configuration-led accelerated release.
Module-by-module compliance against the seven AIPMS-FRS-001 v2.0 modules	Covered under **Compliance Summary by Module** and **Detailed Module Delivery Notes**, stating the delivery method for each module and how Mandatory and High-priority requirements will be addressed in scope.
Configuration Panel approach	Covered under **Configuration Panel Design**, describing how Tier 1 users will maintain programme and financial parameters without direct code changes.
HR module detailed approach	Covered under **Detailed Module Delivery Notes**, **HR Module Delivery Approach**, and the security and access-control sections, including payroll rules, statutory deductions, bulk onboarding, attendance, and restricted payroll data visibility.
FDT integration detailed approach	Covered under **FDT Integration Delivery Approach** and the technical requirements mapping, including CSV import, validation, duplicate checks, batch logging, discrepancy handling, and optional API extension.
System architecture, hosting, security, backup, and recovery	Covered under **Technical Requirements Mapping**, **Recommended Hosting and Recovery Approach**, and **Architecture, HR, and Data Control Notes**.
Offline capability / low-connectivity operating model	Covered under **Offline & Mobile**, which defines the low-connectivity operating position for designated HR field activities and the sync model after reconnection.

C.1 Proposed Delivery Model

Proposed Delivery Model

Inspired Delta Ltd proposes a hybrid AIPMS implementation: ERPNext provides the base platform for projects, workflows, documents, procurement, HR, payroll, and reporting; custom Frappe components provide the AIPMS-specific Configuration Panel, payment certification workflows, FDT ingestion, additional dashboards, and field-level governance controls. This is the fastest route to operational readiness while preserving flexibility for future programme changes.

C.2 Why ERPNext Enables a Lite Version by Week 2

The credibility of the proposed Lite Version depends on whether the underlying platform already contains the core behaviours required for programme commencement. ERPNext makes the Week 2 Lite target realistic because the first release is not a greenfield software build; it is a controlled configuration of mature modules already capable of handling records, workflows, approvals, documents, notifications, dashboards, and role-based permissions.

For AIPMS, the Lite Version is deliberately focused on Modules 1-5 at core operational level. That means the goal in Weeks 1-2 is not to finish every advanced automation, but to stand up the minimum live controls the programme needs to begin safely: milestone tracking, contract register, claim workflow, document repository, governance records, and baseline RBAC.

ERPNext accelerates this because it already provides the structural building blocks we would otherwise spend weeks writing from scratch: workflow engine, role model, document attachments, print formats, notification rules, list and form views, report framework, and audit-oriented transactional records. Our work in the Lite phase is therefore largely configuration, field design, print/output setup, and approval-path alignment rather than low-level application engineering.

That distinction matters in procurement terms. We are not proposing to use ERPNext as a generic label; we are proposing to use it as a delivery accelerator. The platform already gives us the object model, user administration, workflow states, dashboard widgets, report engine, email alerts, attachment controls, comment trail, and permission system needed to launch an operational first release. Because those foundations already exist, the early project effort can focus on configuring AIPMS-specific behaviour rather than constructing commodity platform features.

In practical terms, this means the Week 2 release is credible because the work sequence is front-loaded around setup activities that ERPNext handles well: defining master data, mapping roles, creating the required DocTypes and fields, configuring workflows, applying print formats, loading reference records, and exposing operational views for programme teams. More complex items such as deep validation rules, advanced payment logic, richer FDT reconciliation, or highly tailored analytics can then be layered in during the subsequent sprints without blocking early programme commencement.

How ERPNext Shortens the Lite Release Path

ERPNext is especially suitable for accelerated government and programme delivery where a controlled operational release is required before every enhancement is complete. Its architecture allows us to work in layers: first establish master data, transactions, approvals, and reporting; then add specialised programme controls once live operations have started. This supports the exact AIPMS requirement of making Modules 1-5 usable early while still progressing toward a more fully tuned production platform.

For AIPMS, the Lite Version will be assembled using a mix of standard ERPNext capability and focused Frappe extensions. Standard capability covers the operating spine of the system: users, roles, lists, forms, workflow states, document attachment, assignments, notifications, activity trails, and structured reports. Focused extension work is then reserved for the areas where the RFP is genuinely programme-specific, such as the Configuration Panel, selective approval paths, certificate generation, controlled import of FDT outputs, and executive reporting views.

This approach is lower risk than a fully bespoke build in the same timeframe. A bespoke application would still be spending the first two weeks creating basic scaffolding such as authentication, form behaviour, approvals, document storage, audit trails, and report structure. ERPNext already has those layers, which is why Inspired Delta Ltd can credibly recommend a Lite Version as a working operational platform rather than a demonstration prototype.

Illustrative ERPNext Base Platform Screens

The references below show the kind of standard ERPNext capability that reduces build effort during the AIPMS Lite Version stage: reporting workspaces and project-oriented operational records that can be extended with AIPMS-specific workflow, controls, and reporting

logic.

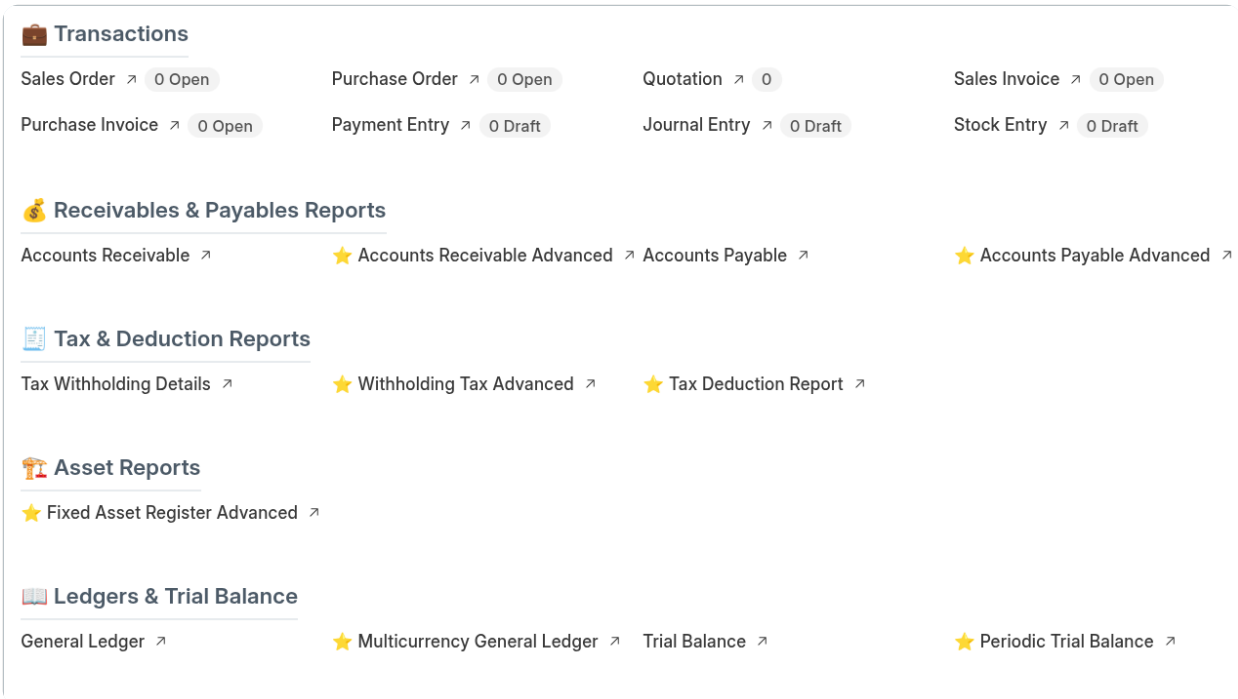

Reporting foundation: built-in reporting workspaces that can be adapted into governance, finance, and operational dashboards.

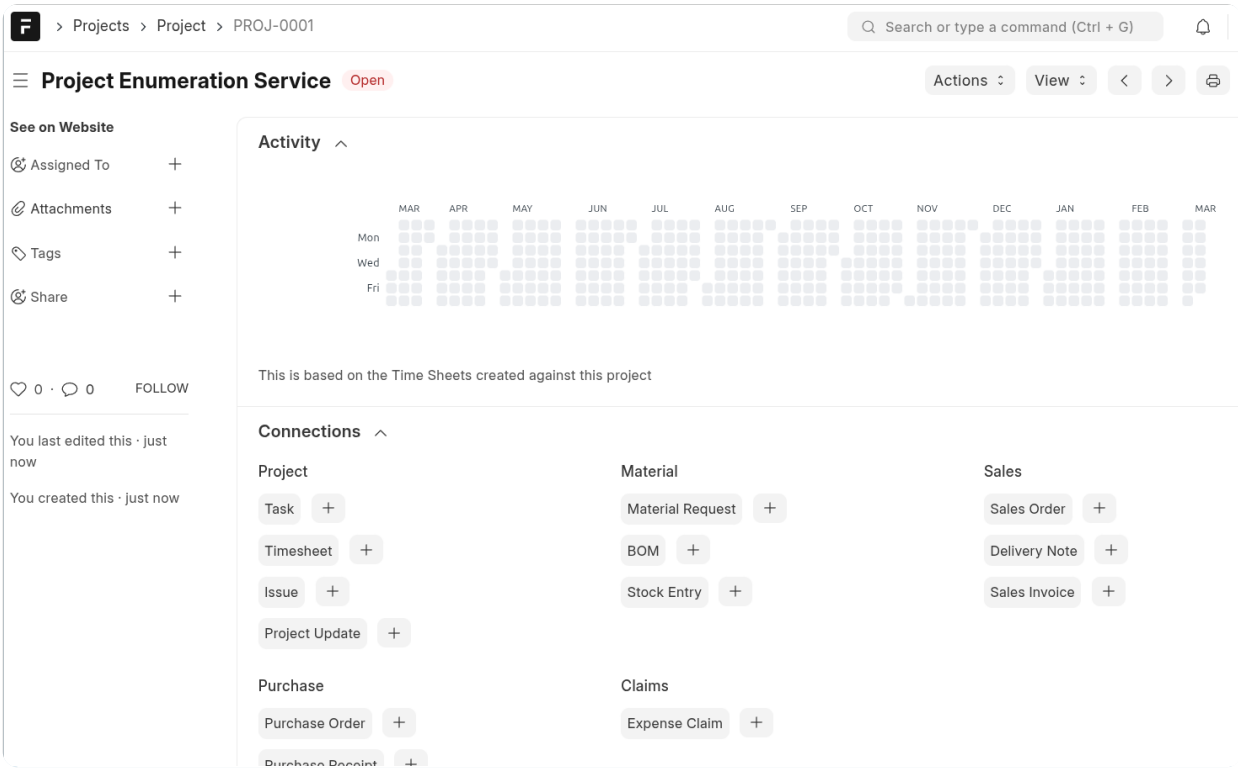

Project workspace: project, task, issue, and claims links that support the schedule and milestone-control model required by AIPMS.

Lite Version Need	ERPNext Capability Already Available	Implementation Impact
Milestone and schedule control	Projects, Tasks, templates, assignments, status tracking, notifications	Configured rather than custom-built, allowing rapid Week 2 activation of Module 1.
Contract and vendor records	Supplier, contract, procurement, workflow, document attachment, reporting framework	Enables Module 2 register and approval structure with targeted custom fields and routing logic.
Payment claim workflow and certificates	Approval workflow, transactional records, print formats, role restrictions	Allows Module 3 core claims and certificate generation to go live before full automation is completed in Phase 2.

Lite Version Need	ERPNext Capability Already Available	Implementation Impact
Document management and audit controls	File attachments, version history, permissions, activity tracking	Supports immediate rollout of repository and approval-linked attachment controls in Lite mode.
Governance and meeting administration	Custom DocTypes, calendars, workflows, notifications, ToDos, reports	Allows meetings, agendas, minutes, decisions, and follow-up actions to be stood up quickly.
RBAC and user provisioning	Role-based permission model, user management, field-level restrictions, approval routing	Reduces lead time for access control because the core security model already exists.

Week 2 Lite Deliverable	What Users Will Be Able to Do	What Is Completed in Later Sprints
Programme schedule workspace	Create and monitor programme schedules, milestones, owners, due dates, and status changes with dashboard visibility.	Deeper analytics, escalation tuning, and final executive print/report refinements.
Contract and vendor register	Maintain vendors, contract records, values, approvals, and document attachments under controlled access.	Extended variation logic, additional compliance checks, and more advanced exception reporting.
Core claim and certificate workflow	Log claims, route approvals, record supporting documents, and generate baseline payment certificates.	Expanded validation layers, advanced withholding logic, and tighter FDT-linked certification rules.
Document and governance repository	Store agendas, minutes, decisions, attachments, and follow-up records with permissions and approval states.	Additional governance templates, quorum automation, and richer search or dashboard summarisation.
User access and baseline controls	Provision users, apply roles, restrict access by function, and track key actions through the audit trail.	Further field-level restrictions, refined segregation-of-duty rules, and operational hardening.

Week 2 Lite Version Positioning

Inspired Delta Ltd positions the Lite Version as a**configuration-led operational release**, not as a claim that all seven modules will be fully completed within two weeks. The delivery sequence is as follows:

- **Week 1:** mobilise, load parameters, create users, define workflows, prepare print formats, and configure the core data model.
- **Week 2:** activate Modules 1-5 for live use at core level, validate access and approvals, and begin programme operations.
- **Weeks 3-8:** extend the platform into deeper automation, FDT integration, dashboards, HR/payroll completion, and full go-live hardening.

This is exactly the sort of delivery model ERPNext supports well: early operational release through configuration, followed by targeted customisation where programme-specific logic becomes necessary.

Accordingly, the Lite Version will operate as a**usable controlled-release environment** for programme commencement, not as a reduced demonstration. Users will be able to transact, route approvals, store evidence, review dashboards, and generate core outputs. The distinction between Lite Version and Full Go-Live is therefore not whether the platform is usable, but the depth of automation, integration maturity, and reporting sophistication available at each stage.

C.3 Configuration Panel Design

The AIPMS Configuration Panel will be implemented as administrator-controlled DocTypes and forms within Frappe. Tier 1 users will be able to maintain contract values, cost lines, working capital advance settings, unit payment rates, zone targets, milestone percentages, retention rules, organisational roles, escalation thresholds, and report parameters without direct code edits. Changes will be permission-controlled and audit-logged.

This design is intended to satisfy the RFP requirement that financial and programme parameters be configurable by authorised users rather than hard-coded into the system. The implementation will therefore expose controlled administrative forms for master settings, approval thresholds, unit rates, milestone percentages, escalation triggers, and report parameters, with change history preserved for governance and audit purposes.

Illustrative Form Configuration Screens

The examples below show the type of no-code or low-code form customisation interface that supports the proposed Configuration Panel approach. They demonstrate how authorised administrators can organise layouts, add fields, and define field properties without rewriting the underlying platform.

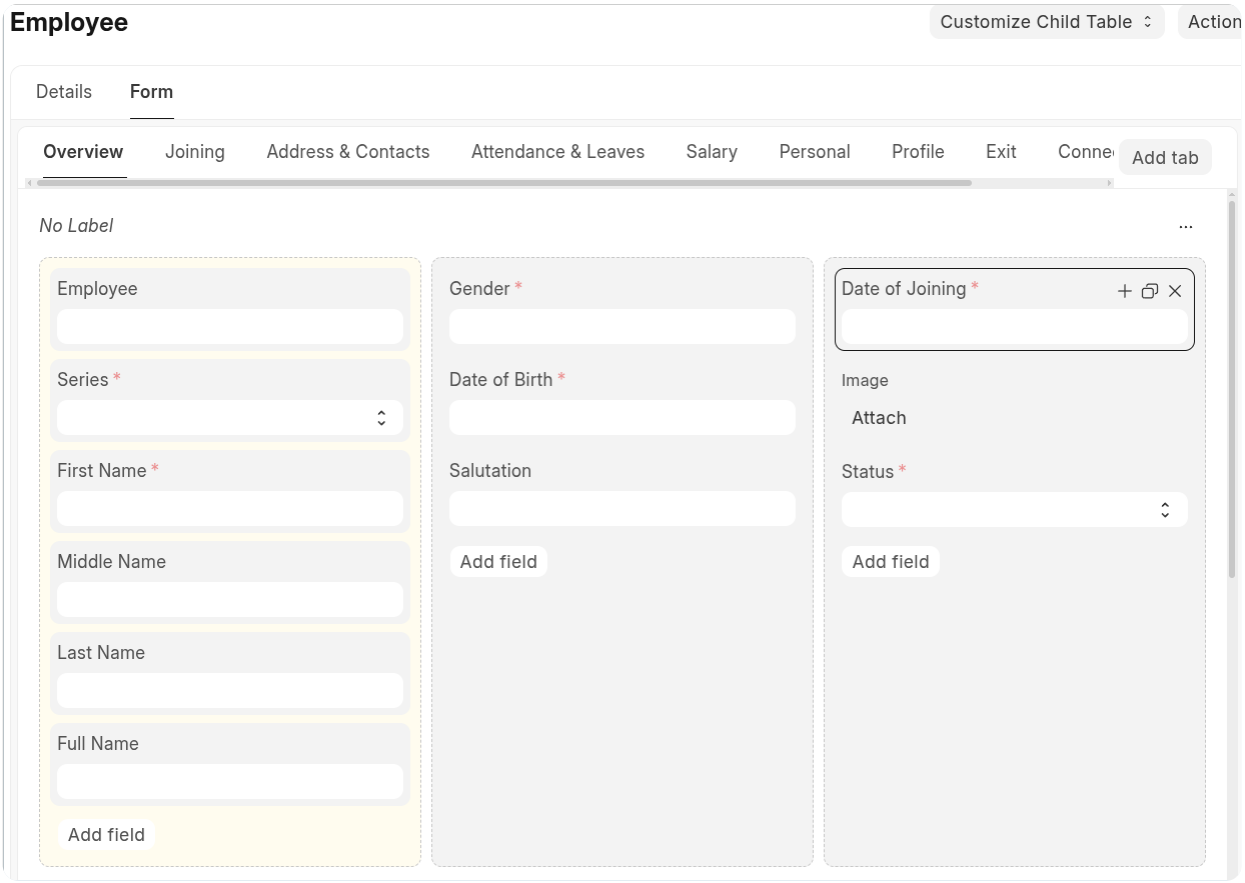

Form layout builder: visual arrangement of tabs, sections, and fields to support controlled AIPMS form design and administrative adaptability.

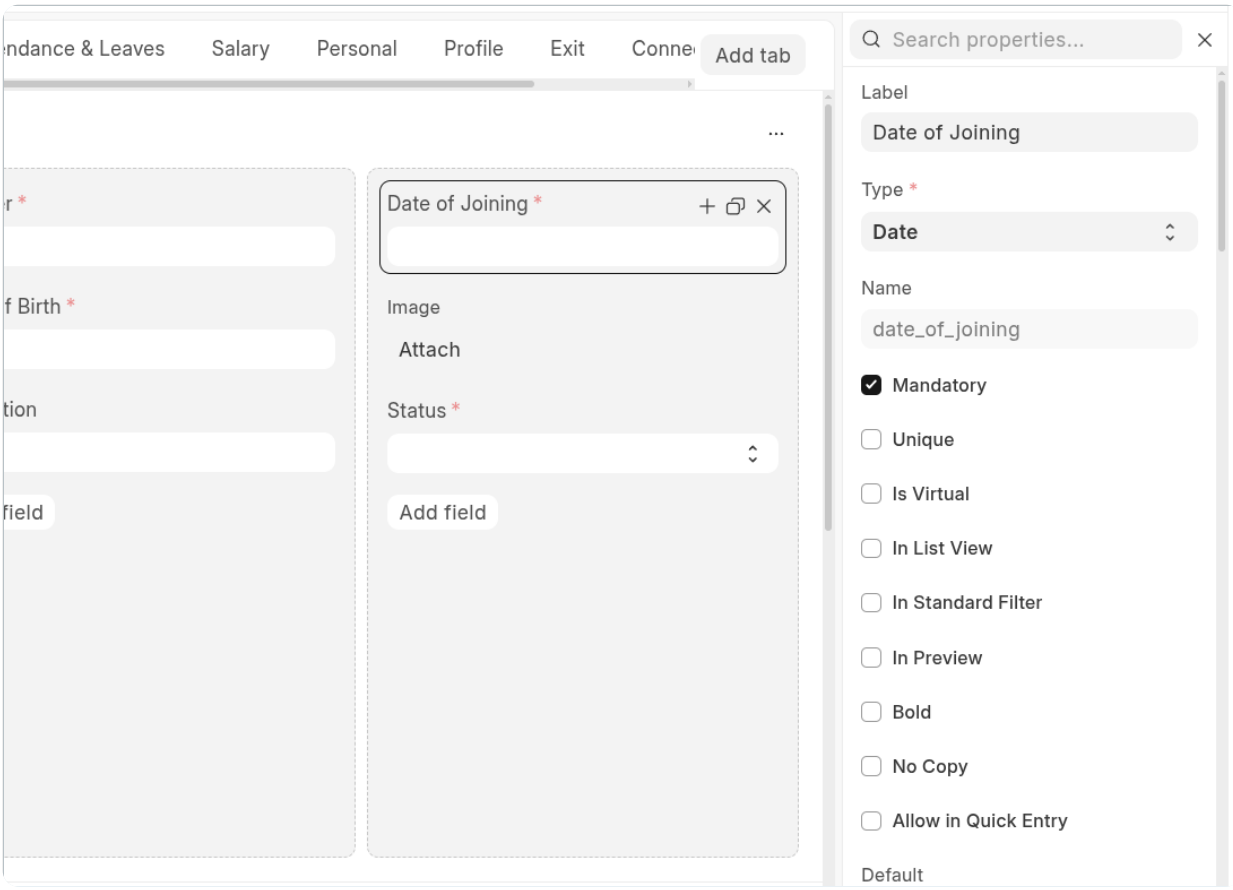

Field property control: configuration of field type, mandatory rules, uniqueness, list visibility, and other administrative properties without custom rewrites for every change.

Illustrative Workflow Configuration Screen

The examples below illustrate how ERPNext workflow states, transition rules, and visual workflow design can be configured for controlled approval progression. In AIPMS, the same design pattern will be used for selective vendor routing, claim approvals, document locking, governance actions, and other programme-specific review states.

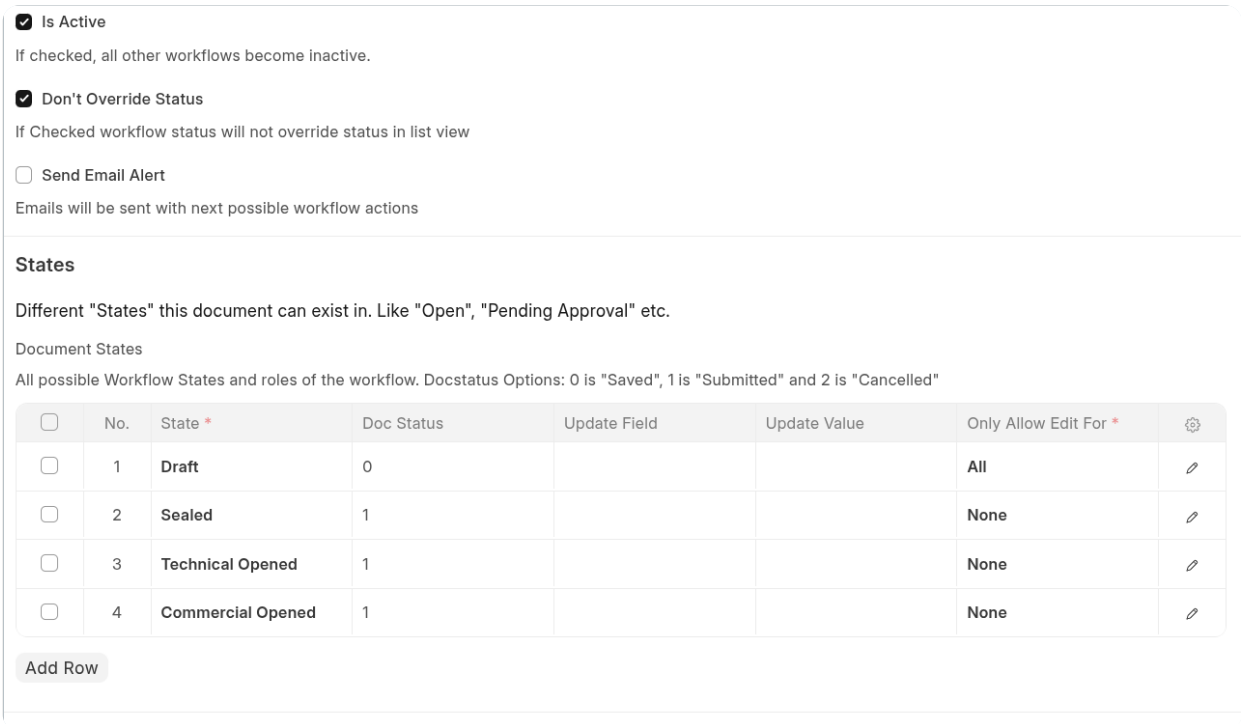

Workflow states: configurable status progression, role restrictions, and approval checkpoints that can be adapted to AIPMS governance and control flows.

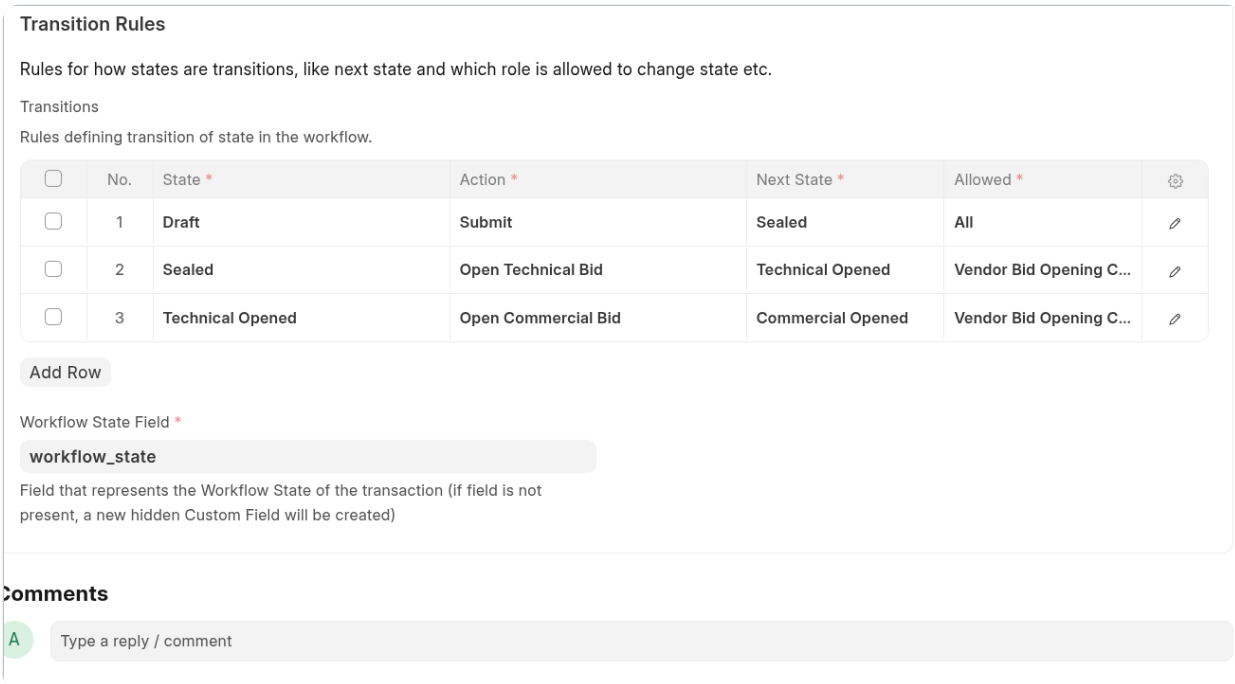

Transition rules: explicit action-to-next-state control showing who can move a record forward and under what workflow condition.

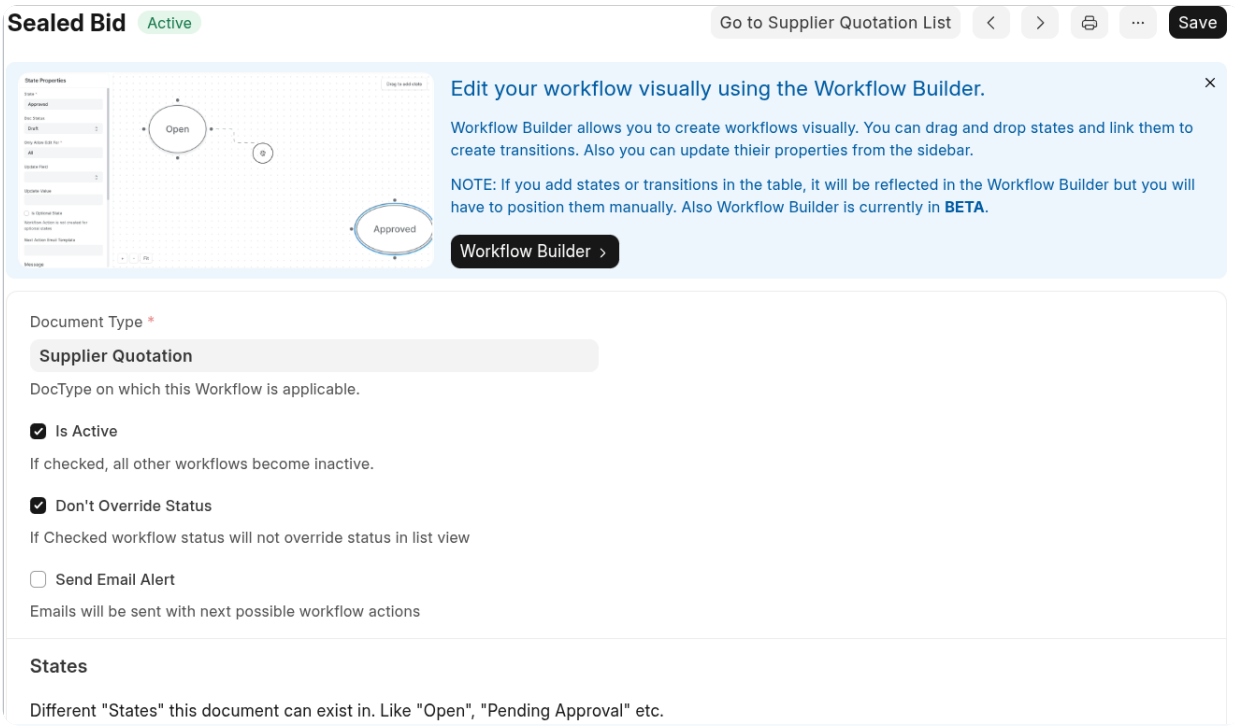

Visual workflow builder: diagram-driven workflow configuration supporting clearer design, review, and future refinement of approval models.

C.4 Compliance Summary by Module

Module	Mandatory / High-Priority Coverage	Delivery Method	Status
1. Milestone & Programme Schedule	Configurable milestones, sign-off workflow, progress tracking, alerts, and live reporting	ERPNext Projects/Tasks plus approval workflow, programme dashboards, and custom milestone reports	**Covered in scope**
2. Contract & Vendor Management	Contract register, SVR workflow, tender control, vendor performance, escalation routing, variation control	ERPNext contracts/procurement with custom SVR, approval routing, escalation register, and variation workflow	**Covered in scope**

Module	Mandatory / High-Priority Coverage	Delivery Method	Status
3. Payment Certification & Drawdown	WCA records, drawdown claims, certificate generation, retention logic, reconciliation, FDT-driven payment checks	Custom AIPMS payment DocTypes, print formats, workflow approvals, and FDT-linked validation logic	**Covered in scope**
4. Document Management & Audit Trail	Versioning, mandatory attachments, immutable approved records, export logging, user action audit trail	ERPNext document model plus custom attachment gates, restricted delete controls, and approval-state locking	**Covered in scope**
5. Governance & Meeting Management	Meeting calendar, agendas, minutes, quorum rules, extraordinary session flow, decision records, sign-off triggers	Custom meeting workflows and agenda/minute records linked to milestones, approvals, and action owners	**Covered in scope**
6. Reporting & Dashboards	Governance dashboard, PMO dashboard, financial reports, FDT import log, PDF/Excel/CSV exports	ERPNext reports/dashboards plus programme-specific print formats and export-ready report views	**Covered in scope**
7. Human Resource Management	Staff records, attendance, deployment, payroll, statutory deductions, training records, CSV onboarding, HR reports	ERPNext HR/Payroll plus custom remuneration rules, field deployment logic, and restricted HR financial fields	**Covered in scope**

Note: The final submission package should include the detailed Annex A line-by-line compliance matrix against AIPMS-FRS-001 v2.0, including treatment of all Mandatory, High, and Desirable requirements.

C.5 Detailed Module Delivery Notes

Module	Detailed Implementation Approach
Module 1: Milestone & Programme Schedule	Programme schedules will be configured through ERPNext Projects, Tasks, Task Types, and Project Templates, with milestone sign-off workflows, real-time progress views, deadline alerts, and milestone status reports generated from live transactional data.
Module 2: Contract & Vendor Management	Contracts will be managed through a structured digital register covering parties, value, dates, amendments, and workflow status. The Selective Vendor Register will be implemented with controlled nomination-to-approval routing, categorisation, escalation handling, and variation-control approval paths.
Module 3: Payment Certification & Drawdown	Custom payment DocTypes will manage working capital advances, drawdown claims, milestone-linked payment logic, payment certificate generation, retention calculations, and reconciliation reporting. FDT imports will be linked to payment validation and discrepancy-hold workflows.
Module 4: Document Management & Audit Trail	Documents will be attached to programme records with version tracking, mandatory-attachment gates for payment and approval steps, approval-state locking to prevent unauthorised edits, and audit visibility over document actions and record changes.
Module 5: Governance & Meeting Management	Meeting records will cover agenda, attendees, minutes, decisions, quorum rules, extraordinary sessions, and follow-up actions. Governance approvals and milestone sign-offs will be linked to downstream payment and reporting processes.
Module 6: Reporting & Dashboards	Dashboards will provide governance, PMO, financial, HR, escalation, and FDT import visibility. Reports will include commitment and variance reporting, workstream progress, payment summaries, import logs, and export-ready outputs in open formats.
Module 7: Human Resource Management	ERPNext HR/Payroll will be configured for employee files, contracts, attendance, deployment, payroll calculation, statutory deductions, training records, and bulk CSV onboarding. Additional controls will handle deployment-linked remuneration and restricted access to salary and bank data.

C.6 AI-Assisted Government Reporting and Variance Review

Inspired Delta Ltd can extend the AIPMS reporting layer with configurable AI-assisted report analysis as a differentiating value-added capability. We have already implemented a comparable pattern in another ERPNext environment using multiple engines, including Claude and DeepSeek, with runtime engine selection, custom

prompts, and report-specific follow-up analysis. The same design can be adapted for AIPMS executive dashboards, financial control reports, payroll or deployment exception reviews, and governance decision support.

This is not positioned as a substitute for formal approvals, audit review, or statutory reporting. Rather, it acts as an analyst-assist layer on top of structured AIPMS reports, helping authorised users identify anomalies, concentration risks, payment exceptions, outlier trends, and follow-up questions more quickly from high-volume report outputs. The differentiator here is that the capability is already proven in a live ERPNext context and can be tuned report-by-report for government oversight use cases instead of relying on generic chat interfaces.

Government Reporting Use Case	How AI Assistance Adds Value
Milestone drawdown and payment certificate review	Summarises unusual variances, missing evidence patterns, repeated discrepancies, or abnormal claim concentrations before management review.
Programme financial oversight	Highlights unusual journal patterns, high-value exceptions, concentration in specific vendors or cost lines, and reconciliations requiring closer scrutiny.
Governance pack preparation	Generates concise briefing notes from dashboard outputs for management and steering committee review, with traceability back to the source report.
HR and payroll exception monitoring	Flags unusual attendance, deployment, remuneration, or deduction outliers for authorised HR reviewers before payroll finalisation.
Field and zone performance reporting	Summarises underperforming zones, delayed milestones, repeated import issues, and trend exceptions requiring operational escalation.

Illustrative AIPMS Insight	Example of What the User Could Receive
Payment certification anomalies	"Zone B claims are 22% above configured unit-rate expectation for the same milestone stage; three certificates also lack the usual attachment pattern. Review before approval."
Vendor concentration and escalation risk	"Two vendors account for 68% of current drawdown value in the North corridor. This level of concentration is materially above the programme average and may warrant management review."
Milestone slippage summary	"Nine milestones are now beyond target date, with repeated delays concentrated in Zones C and F. The common blockers appear to be unresolved approvals and incomplete field evidence imports."
HR and deployment exception review	"Attendance records for one deployment cluster show an abnormal late-arrival spike relative to prior weeks; cross-check deployment roster changes and transport or field access constraints."
Governance briefing note	"This week's governance summary shows stable payment integrity overall, but highlights increased variance in retention deductions and four outstanding action items from the last steering review."
FDT import quality insight	"Import success remains high, but duplicate and exception rows are concentrated in one contractor submission template, suggesting recurring source-data quality issues rather than isolated upload errors."

Why This Matters for Government Oversight

Government programme teams often do not struggle because reports are unavailable; they struggle because there are too many reports, too many exceptions, and too little time to identify what actually needs attention. The AI-assisted reporting layer is designed to compress large structured reports into actionable management observations while preserving traceability back to the original records and dashboards.

For AIPMS, that means authorised users can move faster from raw output to informed review questions such as: which zones are drifting, which claims look unusual, which payroll or attendance patterns need verification, which vendors need scrutiny, and what should be escalated into the next governance session.

Illustrative AI Reporting Screens

The examples below show a working multi-engine AI reporting pattern already implemented by Inspired Delta Ltd in another ERPNext environment. For AIPMS, the same approach can be adapted for government-specific dashboards and exception reports while keeping human review and approval control with authorised users.

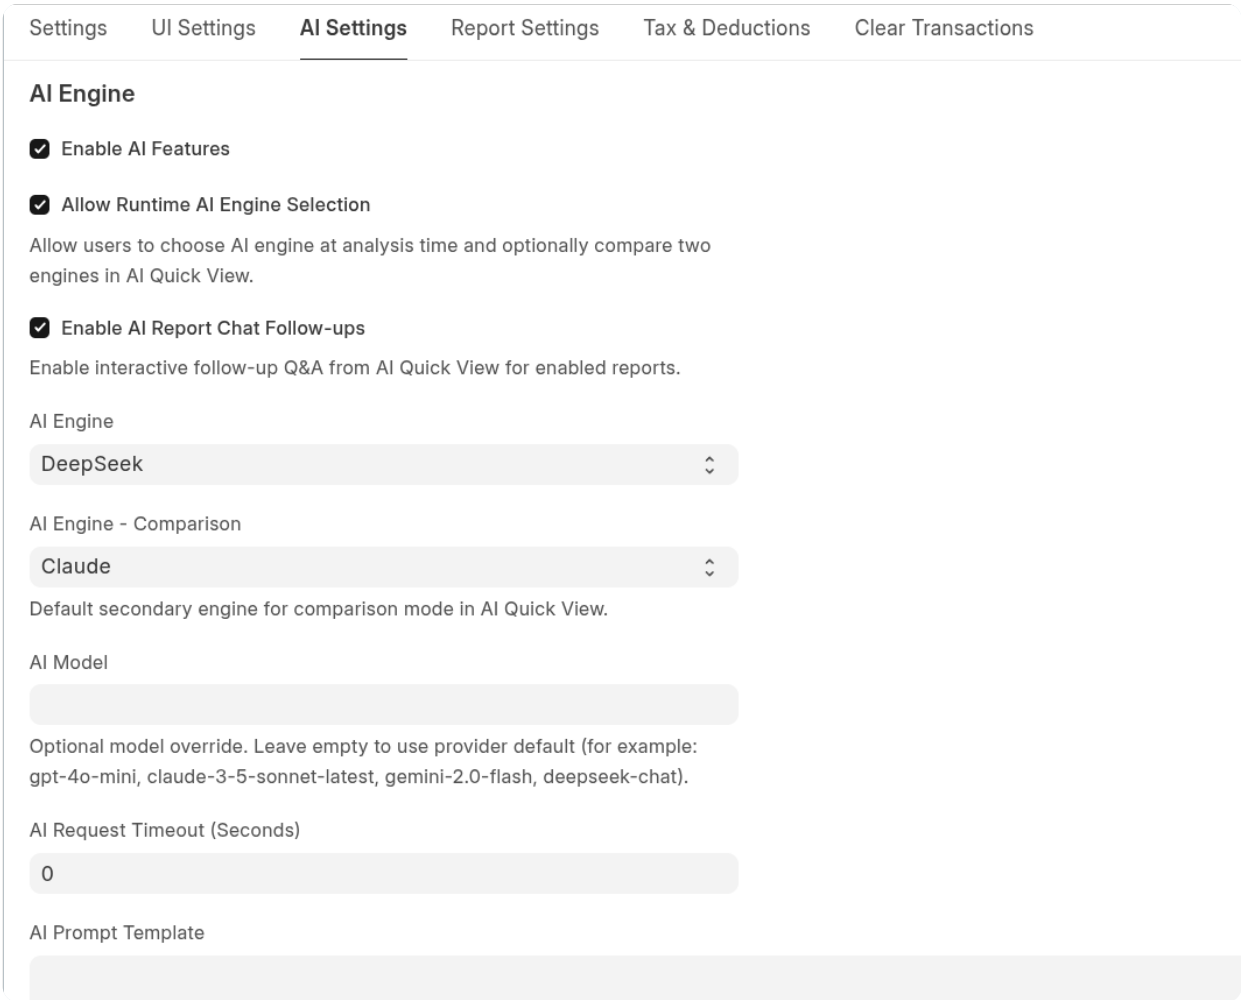

Configurable engine layer: runtime selection of primary and comparison engines with space for additional models as reporting needs evolve.

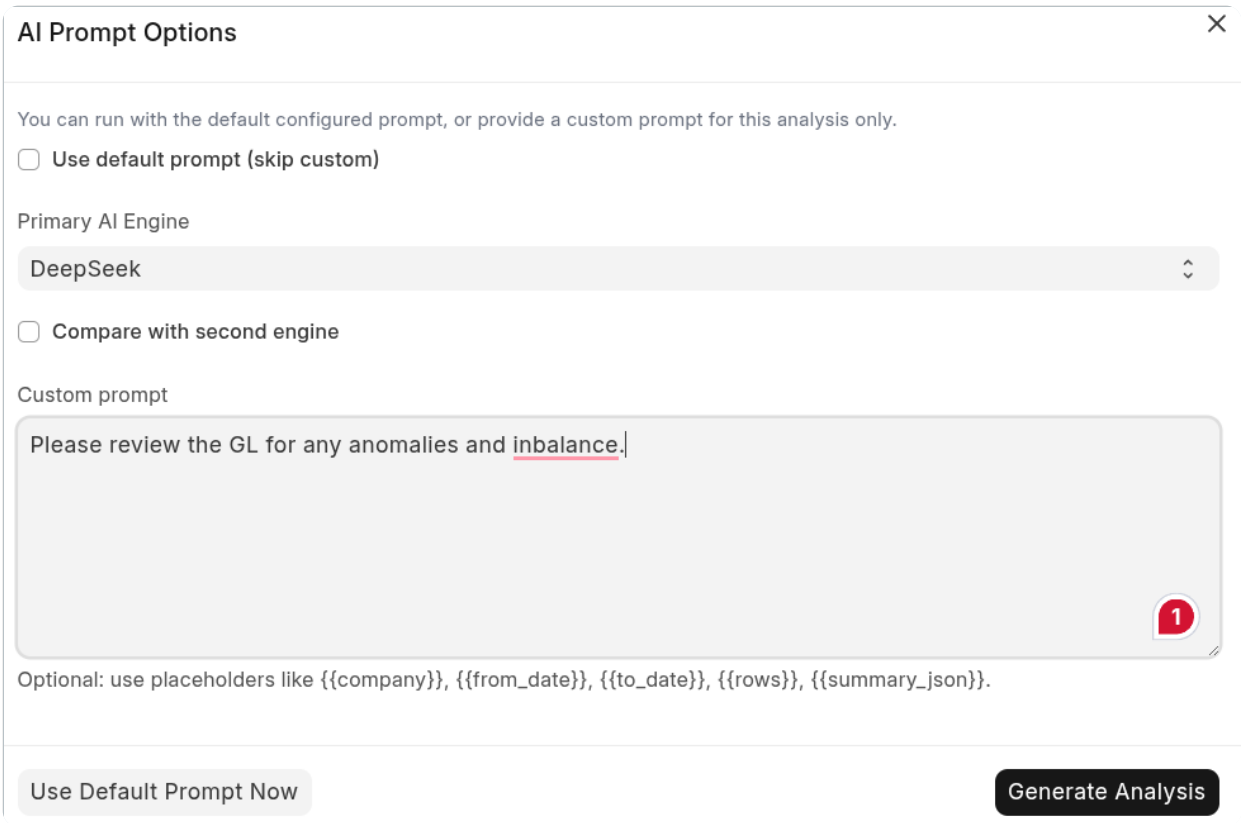

Report-specific prompting: custom prompt options allowing authorised users to tailor the type of analytical review required for a given report.

AI Quick View - General Ledger Multicurrency

Continue asking follow-up questions on this report summary.

Open Follow-up Chat

Engine: DeepSeek | **Prompt:** Custom | **Company** [redacted] | **Period:** 2025-01-01 to 2026-03-14 | **Rows:** 286

Based on the provided GL summary, here are the key observations:

Balances & Integrity:

- ✅ **Debits equal credits** for both period activity ([redacted]) and closing balances ([redacted]).
- ✅ **Net movement is zero** and closing balance is `0.0`, confirming the ledger is mathematically balanced.

Potential Review Points:

1. **Top Account Concentration** – Revenue account [redacted]Services) represents **~99.7%** of total period credits (`46,
   extreme concentration warrants validation of revenue recognition and supporting documentation.
2. **Large Debit to Retained Earnings** – Account `310010` shows a **debit movement of `22,367,903.79`** (unusual as retai
   could indicate dividends, prior-period adjustments, or losses; verify the nature of these entries.
3. **High-Cost Accounts** – Review the largest expense accounts (e.g., `600064` – Ullage/Tariff at `9.2M`, `607501` – Royalty
   alignment.

Recommendations:

- Scrutinize journal entries fo[redacted] for accuracy and authorization.
- Ensure expense accounts are consistently accrued and reconciled with operational reports.
- Confirm all intercompany or partner transactions (e.g., with SHELL) are properly eliminated if applicable.

The ledger is technically balanced, but the anomalies in account movements require substantive review.

Executive quick view: AI-generated observations, review points, and recommendations from a structured report, suitable for adaptation to AIPMS oversight use cases.

C.7 HR Module Delivery Approach

The HR module will be implemented using ERPNext HR and Payroll as the foundation, extended where required for programme-specific deployment controls. This allows AIPMS to support employee master records, contract terms, attendance, deployment assignment, payroll processing, statutory deductions, training records, and bulk onboarding from CSV within a single governed environment.

Our approach is to configure payroll structures, salary components, deduction rules, and approval controls early in the build, then complete detailed remuneration logic and parallel validation before production use. Access to salary, bank, and statutory information will be restricted through role-based and field-level permissions, while line managers and deployment supervisors will only see the operational information required for assignment and attendance administration.

The proposal therefore treats the HR module as a controlled operational subsystem, not a standalone payroll tool. It will be integrated into the wider AIPMS governance model so that staff deployment, attendance, payroll readiness, and reporting remain visible to authorised programme administrators without exposing protected personal or financial data unnecessarily.

Illustrative HR and Claims Screens

These examples show the type of standard HR and controlled-claims forms that can be configured and extended for AIPMS staff administration, attendance-related requests, reimbursements, advances, and payroll-adjacent controls.

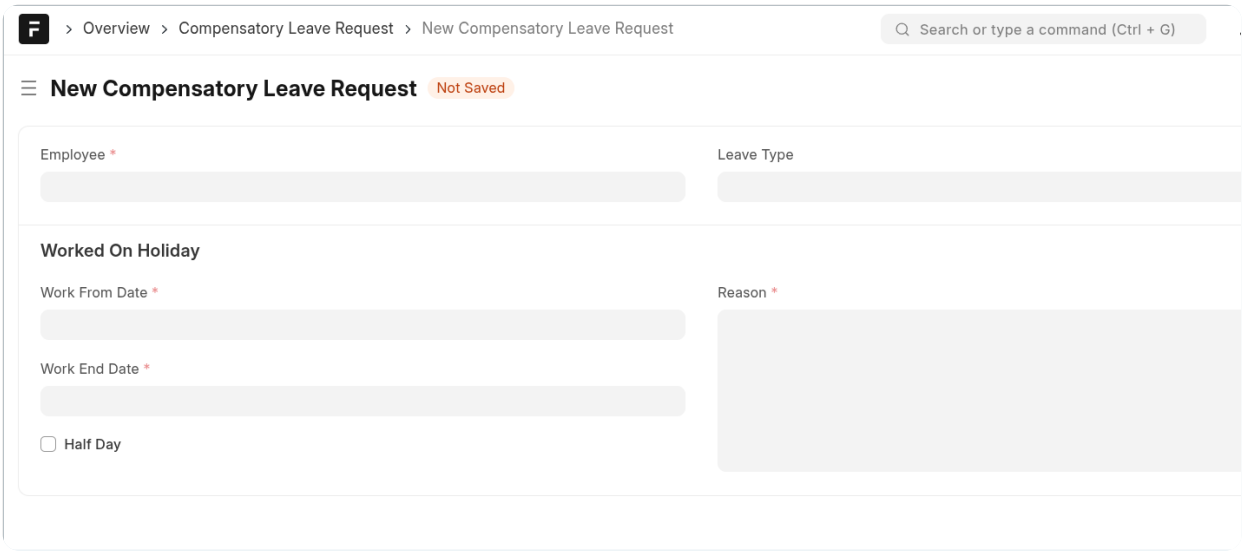

Structured HR form: an example of a controlled request form with required fields, dates, and reason capture.

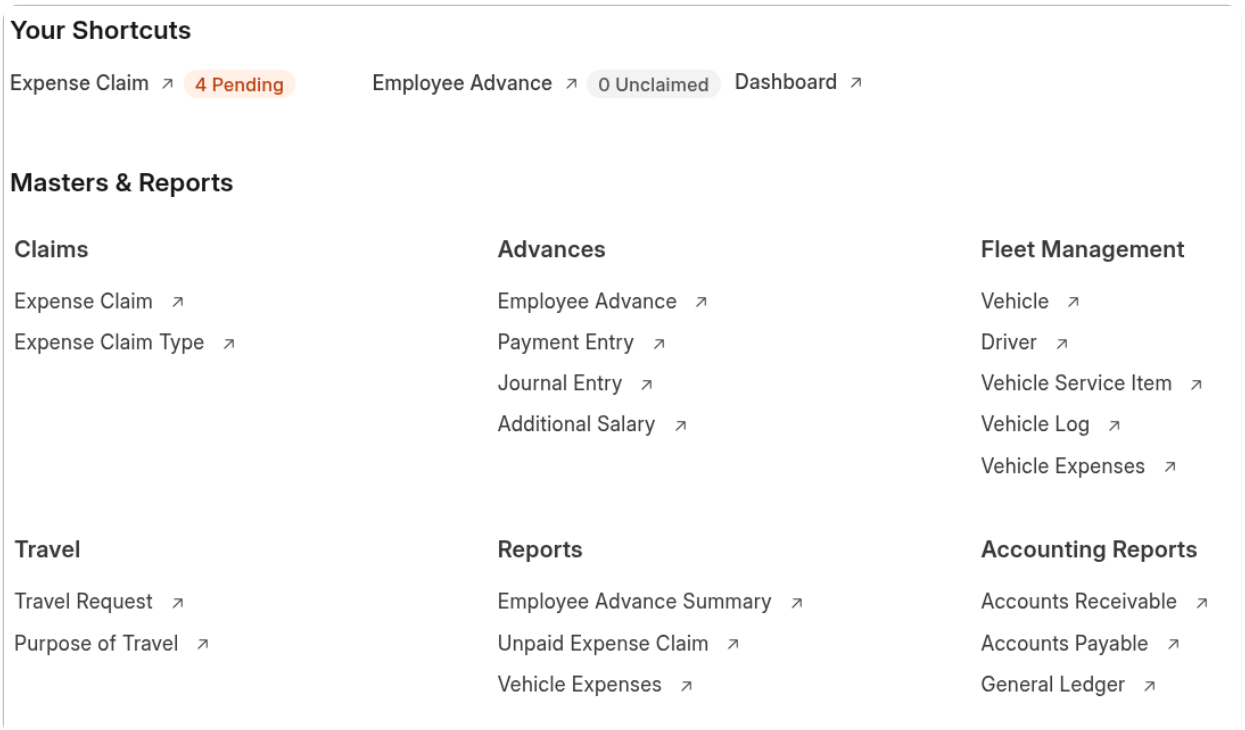

Claims and advances workspace: standard employee expense and advance controls that can be aligned with approval and audit requirements.

C.8 FDT Integration Delivery Approach

AIPMS does not replace the Field Data Tool. Inspired Delta Ltd will implement the required interface layer so that AIPMS can receive, validate, log, and apply FDT outputs in support of certification, reporting, and programme control workflows. The initial in-scope method is controlled CSV-based ingestion, with optional API-based integration available as a later enhancement if the final FDT specification permits.

Our Phase 1 approach covers schema validation, mandatory-field checks, duplicate detection, import batch logging, row-level error reporting, and reconciliation controls so that invalid or inconsistent records do not silently enter payment or reporting processes. Imported FDT outputs will be retained as source records, with discrepancy flags and exception handling used to protect downstream certification workflows.

This means the AIPMS implementation will provide a governed interface rather than a blind file upload utility. The intent is to make FDT-driven decisions traceable, reviewable, and defensible from an audit perspective, especially where imported field results affect payment certification, milestone evidence, or executive reporting.

Illustrative Controlled Import Screen

The examples below illustrate the kind of structured import process that supports the proposed FDT integration model: a source data sheet prepared for controlled upload, followed by template-driven import, review, and visible processing logs.

A	B	C	D	E	F	G	H	I
Sr	ID	docstatus	Account Name	Account Number	Parent Account	Root Type	Report Type	Account Type
1	1000	0	Assets	1000		Asset	Balance Sheet	
2	1100	0	Cash and Bank	1100	Assets	Asset	Balance Sheet	Cash
3	1110	0	Main Programme Bank Account	1110	Cash and Bank	Asset	Balance Sheet	Bank
4	1120	0	Project Float / Imprest	1120	Cash and Bank	Asset	Balance Sheet	Cash
5	1200	0	Receivables and Advances	1200	Assets	Asset	Balance Sheet	
6	1210	0	Working Capital Advance Receivable	1210	Receivables and Advances	Asset	Balance Sheet	Receivable
7	1220	0	Staff Advance Receivable	1220	Receivables and Advances	Asset	Balance Sheet	Receivable
8	1230	0	Vendor Recovery Receivable	1230	Receivables and Advances	Asset	Balance Sheet	Receivable
9	1240	0	Prepaid Hosting and Support	1240	Receivables and Advances	Asset	Balance Sheet	
10	1300	0	Programme Operations Assets	1300	Assets	Asset	Balance Sheet	
11	1310	0	ICT Equipment	1310	Programme Operations Assets	Asset	Balance Sheet	Fixed Asset
12	1320	0	Office Equipment	1320	Programme Operations Assets	Asset	Balance Sheet	Fixed Asset
13	1330	0	Software Licences	1330	Programme Operations Assets	Asset	Balance Sheet	Fixed Asset
14	1400	0	Other Current Assets	1400	Assets	Asset	Balance Sheet	
15	1410	0	Withholding Tax Recoverable	1410	Other Current Assets	Asset	Balance Sheet	Tax
16	1420	0	VAT Input Recoverable	1420	Other Current Assets	Asset	Balance Sheet	Tax
17	2000	0	Liabilities	2000		Liability	Balance Sheet	
18	2100	0	Payables	2100	Liabilities	Liability	Balance Sheet	Payable
19	2110	0	Trade Creditors	2110	Payables	Liability	Balance Sheet	Payable
20	2120	0	Accrued Vendor Certificates	2120	Payables	Liability	Balance Sheet	Payable
21	2130	0	Outstanding Drawdown Claims	2130	Payables	Liability	Balance Sheet	Payable
22	2200	0	Payroll and Staff Liabilities	2200	Liabilities	Liability	Balance Sheet	
23	2210	0	Salaries Payable	2210	Payroll and Staff Liabilities	Liability	Balance Sheet	Payable
24	2220	0	Pension Payable	2220	Payroll and Staff Liabilities	Liability	Balance Sheet	Payable
25	2230	0	PAYE Tax Payable	2230	Payroll and Staff Liabilities	Liability	Balance Sheet	Payable
26	2240	0	NSITF Payable	2240	Payroll and Staff Liabilities	Liability	Balance Sheet	Payable
27	2250	0	NHF Payable	2250	Payroll and Staff Liabilities	Liability	Balance Sheet	Payable
28	2260	0	NHIS / Health Insurance Payable	2260	Payroll and Staff Liabilities	Liability	Balance Sheet	Payable
29	2300	0	Statutory and Tax Liabilities	2300	Liabilities	Liability	Balance Sheet	
30	2310	0	Withholding Tax Payable	2310	Statutory and Tax Liabilities	Liability	Balance Sheet	Tax
31	2320	0	VAT Output Payable	2320	Statutory and Tax Liabilities	Liability	Balance Sheet	Tax
32	2400	0	Retention and Security Liabilities	2400	Liabilities	Liability	Balance Sheet	
33	2410	0	Retention Held on Certificates	2410	Retention and Security Liabilities	Liability	Balance Sheet	Payable
34	2420	0	Performance Security Liability	2420	Retention and Security Liabilities	Liability	Balance Sheet	Payable
35	3000	0	Equity and Reserves	3000		Equity	Balance Sheet	
36	3100	0	Accumulated Surplus / Deficit	3100	Equity and Reserves	Equity	Balance Sheet	

Source worksheet: an example of the type of tabular source data that can be mapped, validated, and prepared for controlled ingestion into the platform.

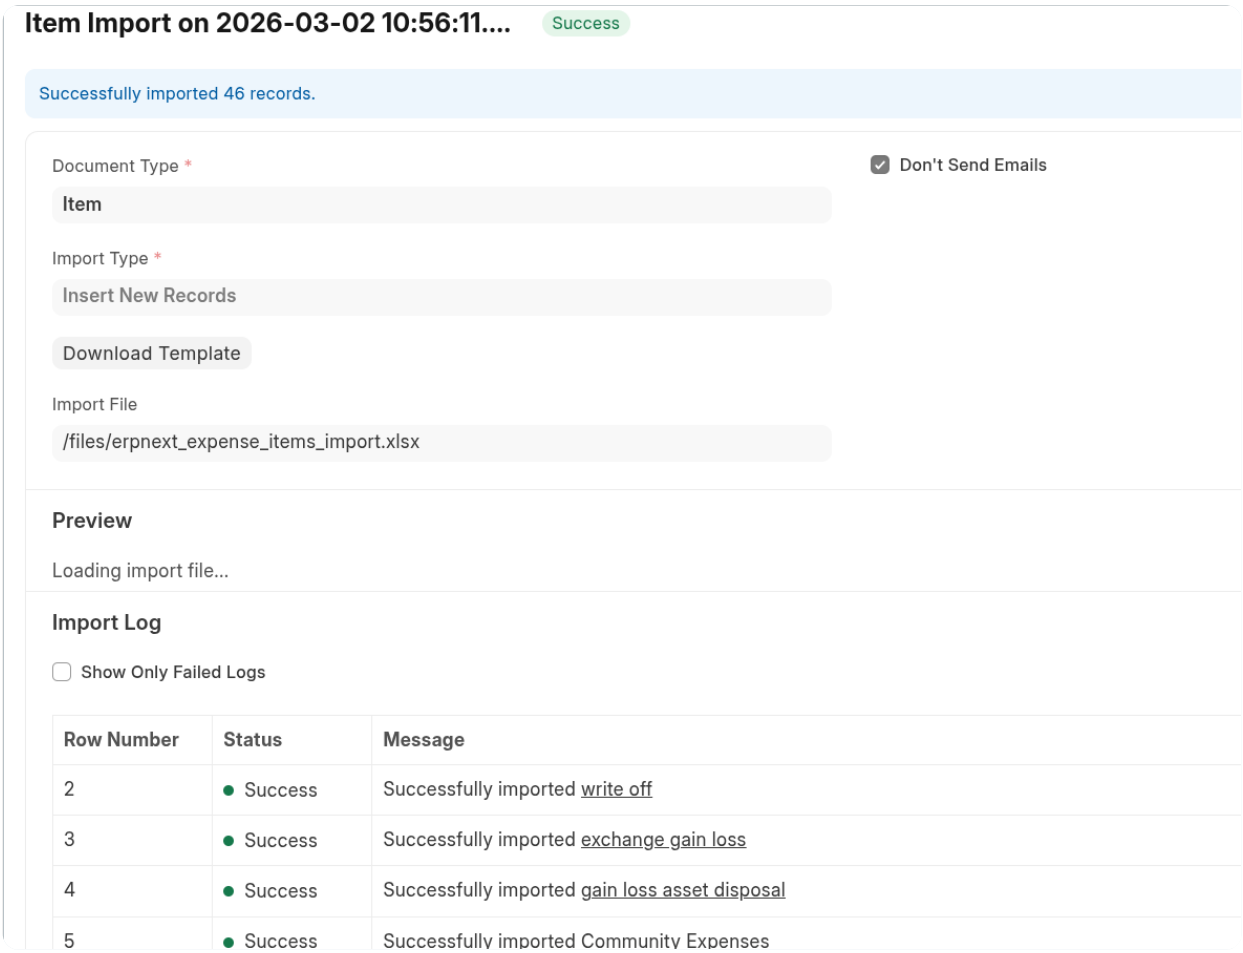

Controlled import workspace: template-based import, processing log, and visible success or failure status aligned with the AIPMS FDT ingestion approach.

FDT Import Requirement	Proposed AIPMS Approach
CSV import interface	A controlled import workspace will be provided for authorised users to upload FDT CSV files against a defined template. The tool will support pre-import validation, import preview, batch submission, and persistent import history so that every load can be traced by file, operator, date, and result.
Validation logic	Validation rules will check file structure, expected headers, mandatory fields, field type conformity, date formats, contract or milestone references, and other business-rule dependencies before records are committed. Invalid rows will be rejected into an exception log for correction and controlled re-import.
Deduplication mechanism	Deduplication will be handled through a combination of batch identifiers, source record keys, and configurable matching rules on agreed business fields such as claim reference, milestone reference, vendor reference, or field transaction ID. Suspected duplicates will be held for review rather than automatically merged or overwritten.
Import auditability	Each import batch will produce a log showing accepted rows, rejected rows, warnings, duplicate flags, user identity, upload timestamp, and downstream processing status. This allows payment and governance teams to review how imported records affected operational workflows.
Phase 2 API approach	If the FDT exposes a stable authenticated interface, Phase 2 can extend the CSV process into scheduled or event-driven API exchange. The recommended pattern is a secure API gateway with token-based authentication, schema-level validation, idempotent processing, error queueing, and reconciliation logs so API ingestion remains as controlled and auditable as batch imports.

C.9 Technical Requirements Mapping

Hosting & Infrastructure

- **Recommended deployment:** cloud-hosted ERPNext/Frappe production environment with primary production data hosted in Nigeria for contractual and data-governance clarity, subject to final client confirmation in the hosting schedule.
- **Availability target:** 99.5% monthly uptime minimum, excluding pre-agreed maintenance windows scheduled outside business hours.
- **Backup strategy:** automated nightly full backups plus transaction-log / point-in-time recovery retention, with backup encryption and routine restore testing.
- **Recovery design:** operational runbook designed to support RPO of 1 hour and RTO of 4 hours for production restoration.
- **Capacity baseline:** initial production sizing for at least 50 concurrent users, with headroom for peak milestone and certification periods and a scale-up path for app and database resources.

Security & Access Control

- TLS in transit and encrypted storage for production data and protected backups.
- 2FA enforced for Tier 1-4 users and configurable for other tiers.
- RBAC at module, record, and field level, especially for HR/payroll data.
- Audit logging for create, update, approval, export, and privileged access events.
- Pre-go-live penetration testing with remediation of critical findings before production sign-off.

C.10 Recommended Hosting and Recovery Approach

Area	Recommended Approach
Production Topology	Dedicated production environment with reverse proxy, ERPNext/Frappe application services, Redis/background workers, MariaDB relational database services, and managed backup storage. Non-production environments will be separated from live production operations, with staging used for controlled release verification before deployment.
Data Residency	Inspired Delta Ltd recommends and prices the solution on the basis of primary production data residency in Nigeria. The final hosting schedule should therefore name the Nigerian production location explicitly, with any secondary backup or disaster-recovery copy managed in line with the agreed contractual and regulatory position.
Backup Operations	Nightly encrypted full backup, point-in-time transaction-log retention, and replicated backup copy to secondary storage. Monthly restore verification should be part of service reporting to prove recoverability, not just backup existence.

Area	Recommended Approach
Recovery Procedure	Documented runbook covering service restoration sequence, database recovery, application verification, user acceptance checks, CI/CD-assisted application redeployment, and communication/escalation steps. This is how the stated RPO and RTO become operationally credible.
Monitoring & Alerts	Infrastructure and application monitoring for uptime, queue health, disk utilization, failed jobs, backup status, and critical workflow failures, with alerting routed to the support lead during hypercare and retainer support.
Scaling Model	Start with right-sized production resources for the expected user base, then scale vertically or horizontally during peak usage windows such as milestone reviews, payroll runs, bulk imports, and reporting cycles.
Business Continuity Position	Inspired Delta Ltd presents backup and recovery as part of an overall operational continuity model: backups, monitoring, restore testing, controlled CI/CD deployment and rollback, escalation workflow, and documented support ownership.

Architecture Area	Specific Recommendation
Hosting environment	Managed cloud deployment with separate production and non-production environments, reverse proxy, application workers, job queues, encrypted object or backup storage, and monitored network access controls.
Database technology	MariaDB is recommended as the primary transactional database for the ERPNext/Frappe deployment, backed by structured backup retention, point-in-time recovery design, and controlled administrative access. Redis will support caching and queue processing.
Security measures	TLS for all client and integration traffic, encryption for backup media, role-based and field-level access restrictions, 2FA for privileged users, audit logging, hardened admin access, and pre-go-live security review with remediation of material findings.
Backup and recovery	Nightly encrypted full backups, transaction-log retention supporting point-in-time recovery, secondary backup copy, documented restoration runbook, and routine restore testing aligned to target RPO of 1 hour and RTO of 4 hours. The recovery approach should also include CI/CD-controlled rebuild and redeployment of the approved application release so infrastructure restoration and code restoration are managed together.
CI/CD and release recovery	Version-controlled build and deployment pipeline for configuration, custom app code, and approved release packages, with staged promotion through non-production environments before production deployment. The same pipeline should support controlled rollback or environment rebuild during disaster-recovery events so restored infrastructure returns to a known approved release state rather than relying on ad hoc manual reconfiguration.
Data residency confirmation	The proposal position is that the primary production environment should reside in Nigeria. Any exception to that should be treated as a commercial and legal approval item rather than left implicit.

FDT Integration Module

- Phase 1 CSV import workspace with upload controls, preview checks, schema validation, duplicate detection, field-level error reporting, and immutable batch logs.
- Imported FDT records retained as source records; payment discrepancies and duplicate candidates flagged for manual review rather than overwritten.
- Phase 2 API option can be provided as an optional enhancement, using authenticated endpoints, idempotent processing, exception handling, and reconciliation logging, subject to the final FDT interface specification.

Offline & Mobile

- Web access across current desktop and mobile browsers.
- Designated HR attendance and deployment forms can be delivered through a lightweight custom PWA-style capture interface built on Frappe APIs, service-worker asset caching, and an offline transaction queue stored in the browser.
- Submitted offline records will be stored locally with a pending-sync state, then queued for synchronisation once connectivity is restored so users and supervisors can distinguish local draft records from server-confirmed transactions.
- Conflict handling will prevent silent overwrites by requiring server-side validation, deduplication, and exception prompts on reconnection before the record becomes part of the central AIPMS dataset.
- Scope includes configuration, testing, device/browser guidance, and user training for low-connectivity operating conditions.

Low-Connectivity Operating Model for HR Attendance and Deployment Forms

For the designated HR attendance and deployment use cases, Inspired Delta Ltd proposes a controlled offline-capable browser workflow delivered as a lightweight custom progressive web application (PWA) rather than unrestricted full-platform offline operation. This is implementable within the Frappe ecosystem as a targeted extension: the installable mobile shell is provided through standard PWA techniques, while the offline submission behaviour is added through a custom queue-and-sync layer connected to Frappe APIs.

The form will expose only the minimum approved attendance and deployment fields required for field operations, and it will be designed to open quickly, cache its shell locally, and continue accepting entries when connectivity is weak or temporarily unavailable. In operating terms, the user first opens the lightweight form while online so the latest form definition, reference values, and user permissions are loaded to the device. If connectivity drops, the user can continue to capture attendance or deployment data and save it locally with a time stamp, user identity, and pending-sync status.

Once connectivity is restored, the queued transaction is synchronised back to the central AIPMS environment through a controlled Frappe endpoint and subjected to the same server-side validation, permission checks, deduplication checks, and audit logging as any directly online transaction. We recommend implementing the queue using a browser-side persistent store such as IndexedDB, with explicit sync states such as Pending Sync, Synced, and Exception so that field users and supervisors can see which records are still local and which have been accepted by the system of record.

This offline approach is intentionally limited to the specific HR forms identified in scope. It is suitable for low-connectivity attendance and deployment administration, and it avoids overstating the proposal as a completely offline ERP environment. The recommended design pattern is consistent with the broader Frappe ecosystem, where mobile-facing products are already delivered through installable progressive web applications even though full offline transaction sync must still be implemented as a custom workflow layer.

Illustrative Mobile HR Experience

The screenshots below illustrate the type of lightweight mobile experience that supports field-friendly attendance workflows: installable access, simple login, quick check-in action, confirmation step, and successful submission state. In the proposed AIPMS model, the same pattern is adapted for designated HR attendance and deployment forms with queued synchronisation where connectivity is unstable.

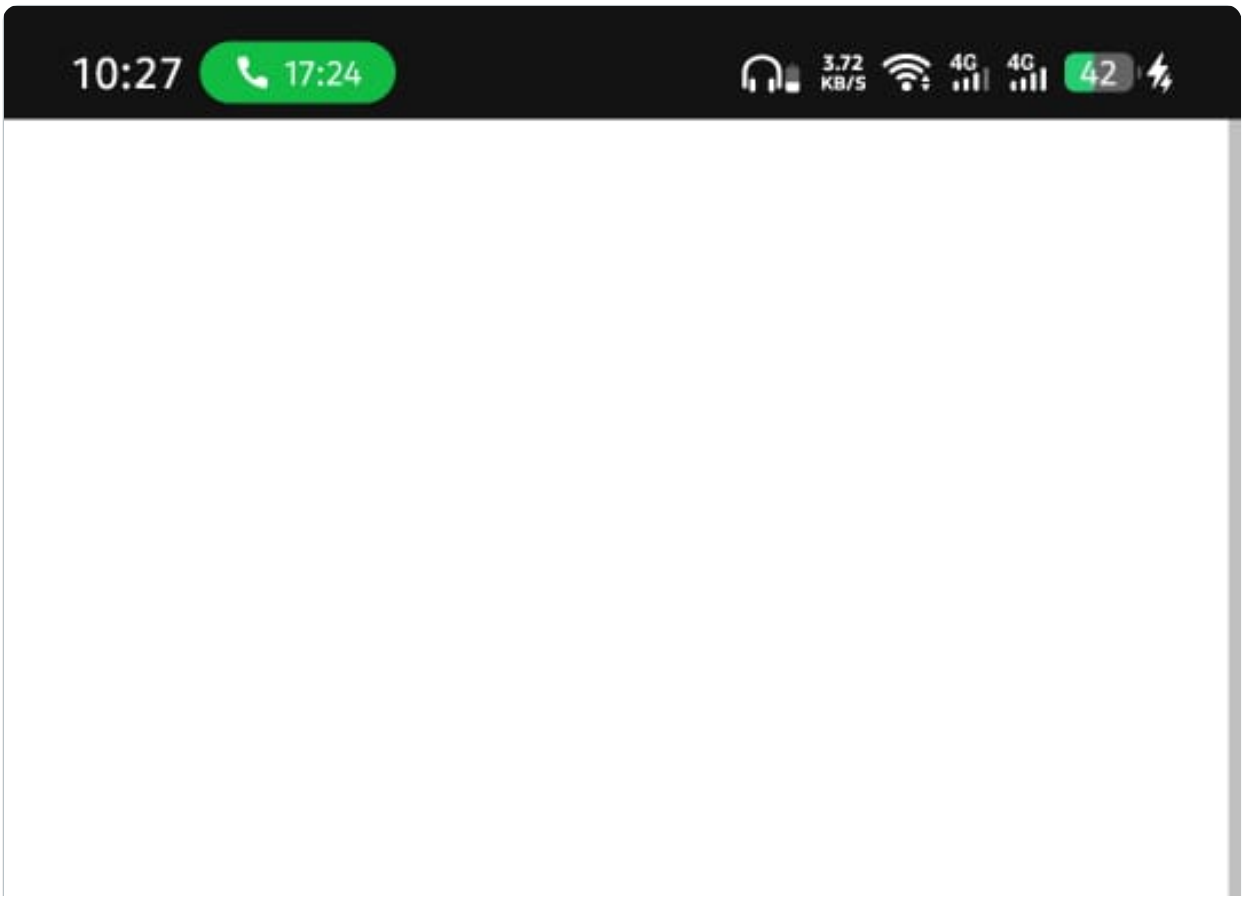

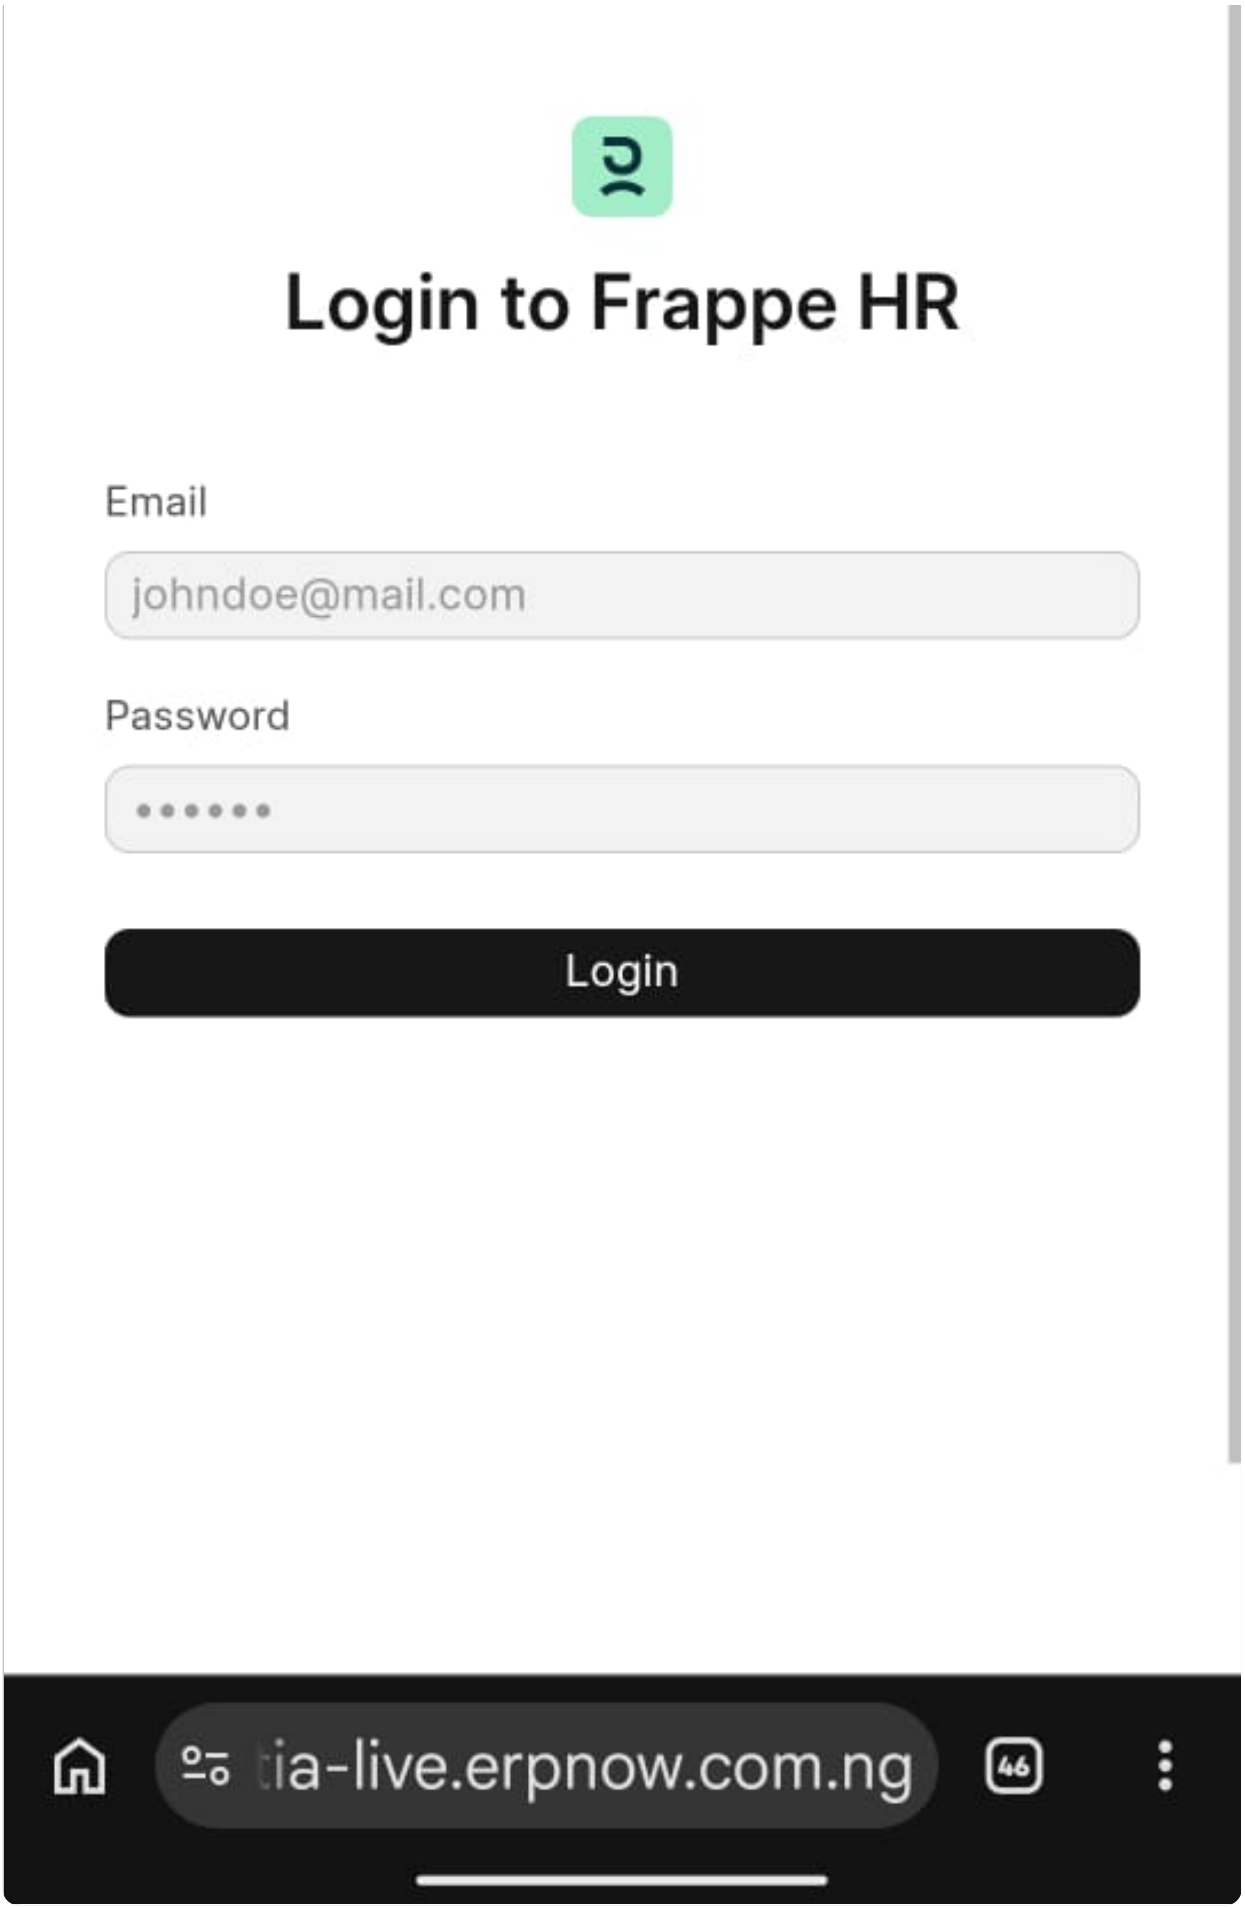

Login and app access: installable mobile-facing screen suitable for rapid user access in the field.

Frappe HR

A

Hey, Adaora 👋

Check In

Quick Links

- Request Attendance
- Request a Shift
- Request Leave
- Claim an Expense
- Request an Advance
- View Salary Slips

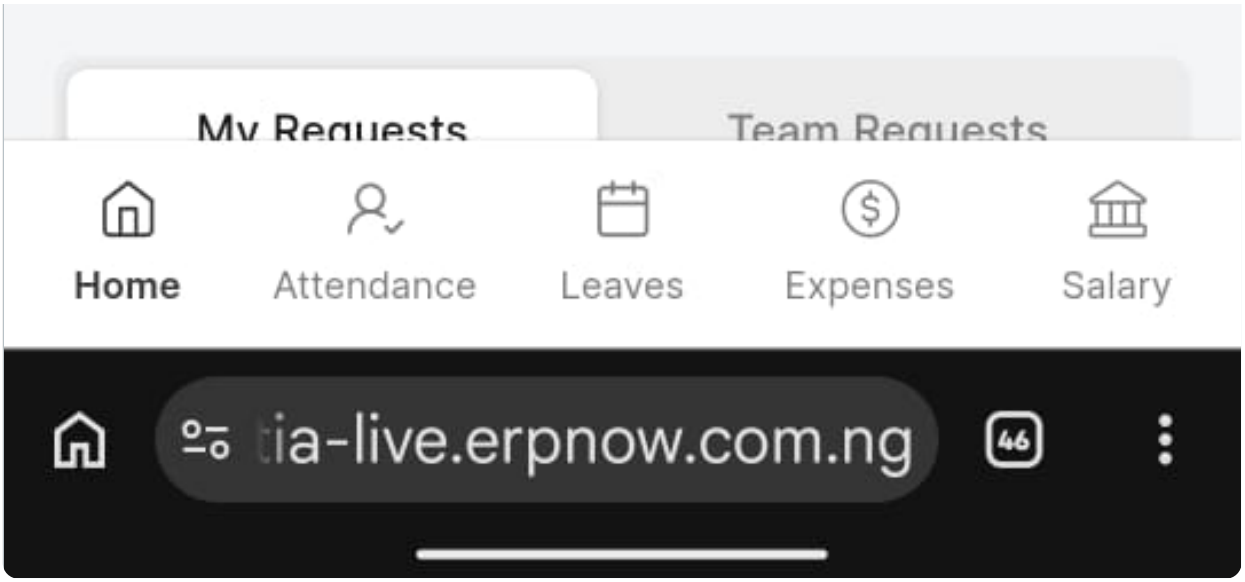

Home and check-in entry: a simplified mobile home screen with a direct attendance action.

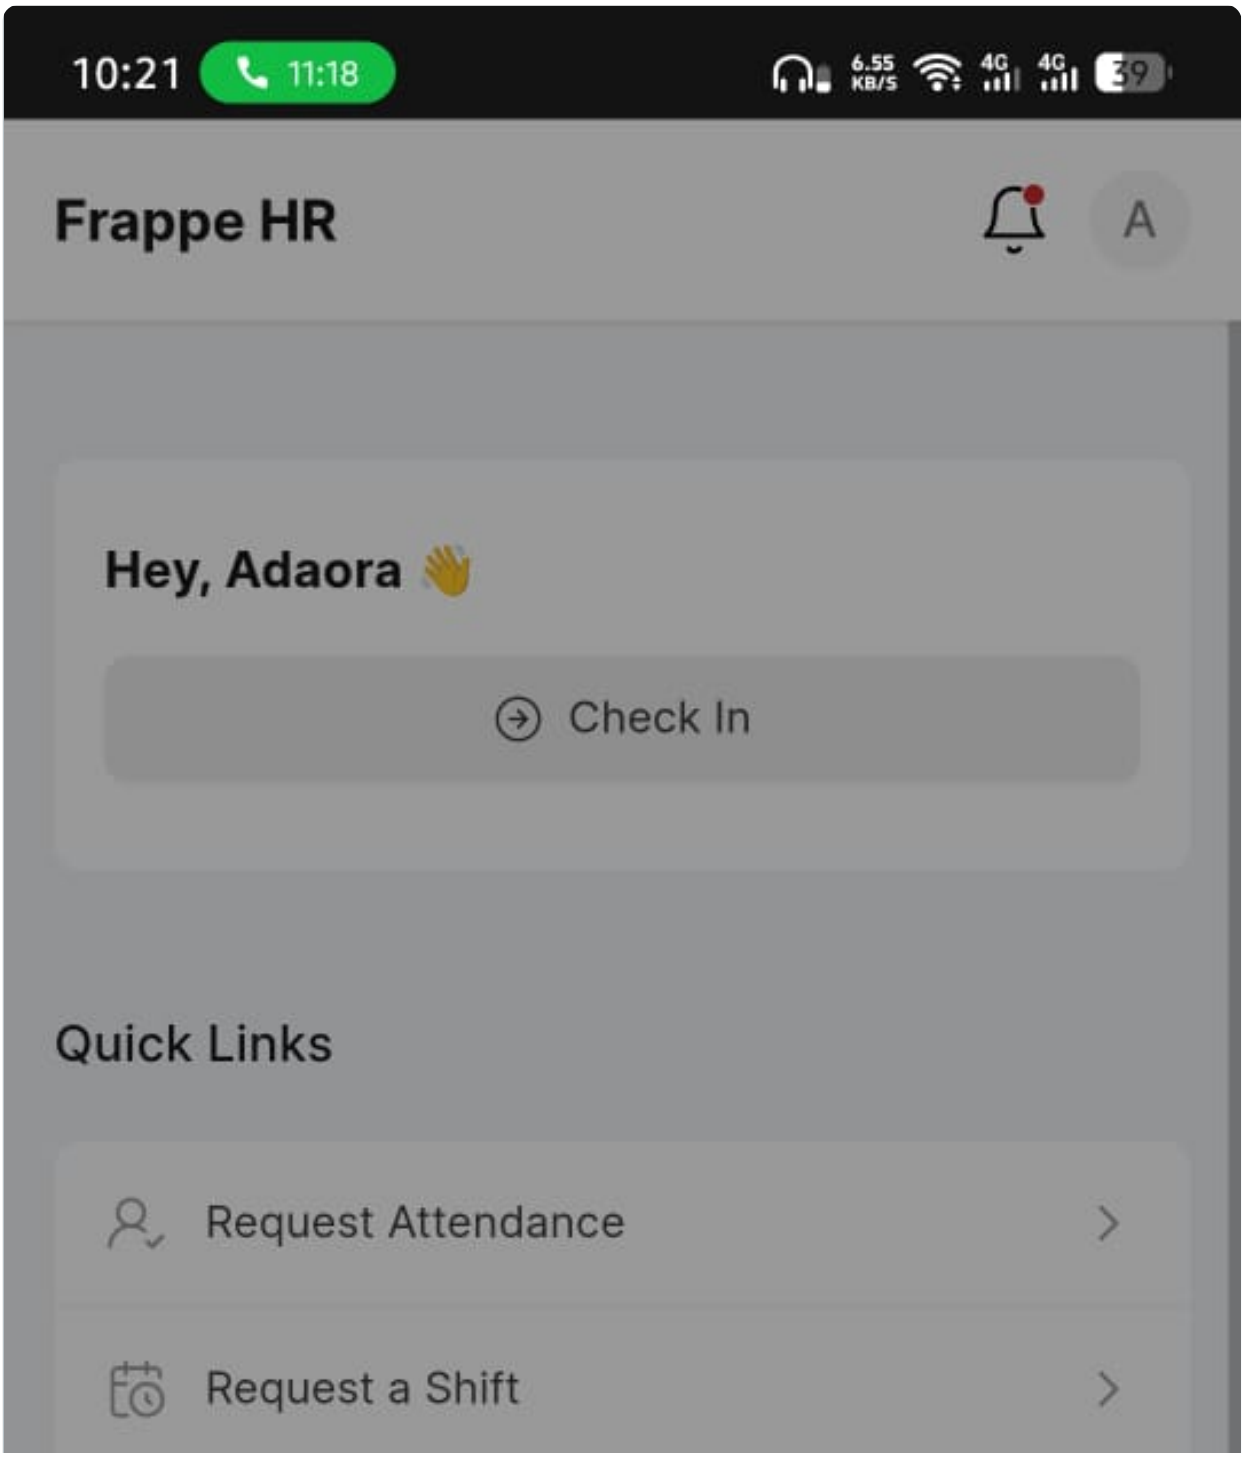

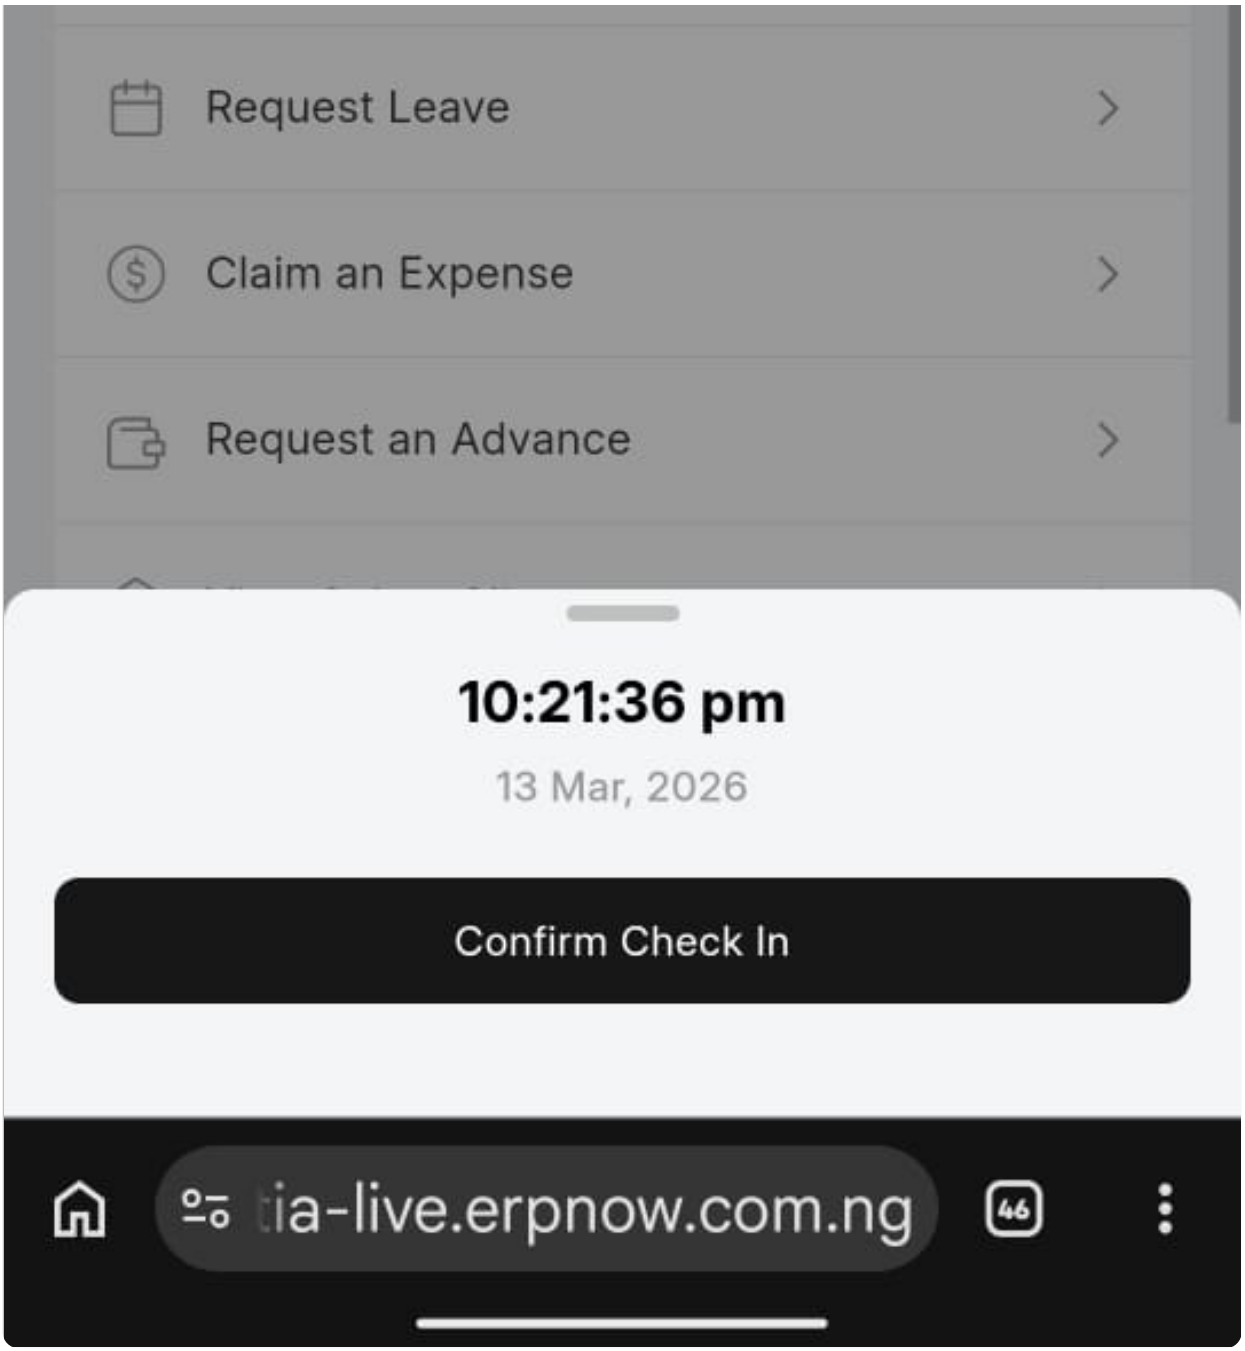

Confirmation step: explicit user confirmation before the attendance transaction is submitted.

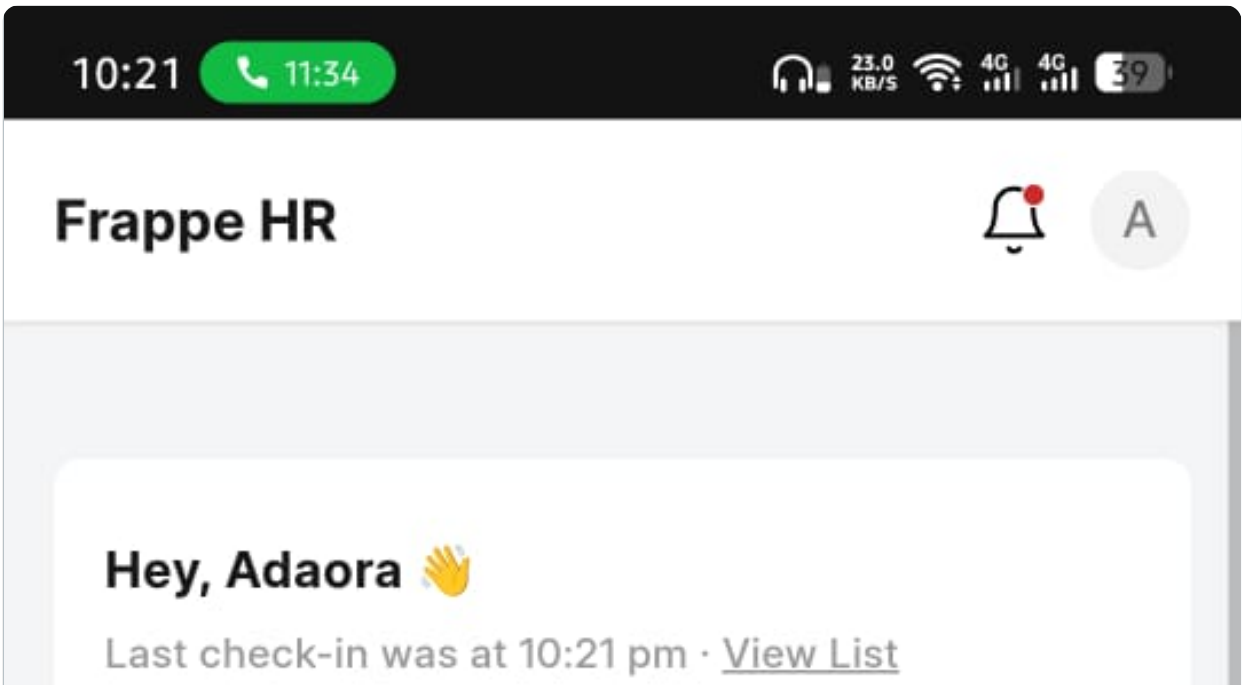

Check Out

Quick Links

- Request Attendance
- Request a Shift
- Request Leave
- Claim an Expense
- Request an Advance
- View Salary Slips

Success

Check-in successful!

Home | Attendance | Leaves | Expenses | Salary

tia-live.erpnow.com.ng

Success feedback: clear confirmation to the user once the attendance action has been accepted.

Low-Connectivity Step	How the Process Will Work
1. Form preparation	Authorised HR or deployment users access the designated attendance or deployment form while online. The system loads the latest allowed form structure, required reference values, user permissions, and validation rules into the browser session.
2. Local capture during low connectivity	If connectivity becomes weak or unavailable, the user can still enter attendance or deployment data into the lightweight form. The data is saved locally in the browser on the device together with a time stamp, user identity, and sync status marker.
3. Local queue and status tracking	Each saved record remains in a pending-sync queue visible to the user or supervisor. This makes it clear which records are still local drafts and which have already been accepted by the central AIPMS platform.
4. Reconnection and submission	When the device reconnects, the queued records are submitted to AIPMS through a controlled API or server endpoint. Submission occurs in sequence so each record can be validated and acknowledged individually.
5. Server-side validation	AIPMS validates the submitted record against current business rules, required fields, user permissions, duplicate checks, and any linked employee or deployment references. Invalid or conflicting records are rejected into an exception state rather than silently accepted.
6. Audit and final confirmation	Accepted records are committed to the live AIPMS database, audit-logged, and marked as synchronised on the user device. Exception records remain visible for correction and re-submission under controlled review.

Supporting Reference Notes

The proposed low-connectivity design is informed by the current Frappe product pattern for installable mobile-facing progressive web applications together with the existing HRMS frontend service-worker implementation. Relevant references include the Frappe HR mobile app installation guide, the Frappe CRM mobile app installation guide, the Frappe framework apps-page guidance for exposing custom app routes, and the HRMS frontend service worker and app bootstrap in the local codebase:

- https://docs.frappe.io/hr/mobile-app-installation
- https://docs.frappe.io/crm/mobile-app-installation
- https://docs.frappe.io/framework/user/en/apps-page
- Local reference: `hrms/frontend/src/main.js` service worker registration
- Local reference: `hrms/frontend/public/sw.js` Workbox-based service worker bootstrap

These references support the technical position that a lightweight installable PWA-style capture interface can sit alongside the main ERPNext/Frappe platform for targeted mobile or low-connectivity workflows, while the offline transaction queue and reconnect synchronisation behaviour are implemented as a controlled custom extension rather than assumed as a default ERPNext feature.

C.11 Architecture, HR, and Data Control Notes

Area	Approach
System Architecture	Multi-tier Frappe/ERPNext application stack with segregated application, database, and backup controls. Final infrastructure diagram to be attached in the technical appendix.
HR Payroll Engine	Payroll configured for fixed and variable earnings, statutory deductions, deployment-linked remuneration, training records, and controlled access to salary/bank fields.
Exports & Exit	Programme data export capability in open formats, with transition support defined in the support and exit provisions. Platform continuity will be documented in the final commercial and legal schedules.
Audit Rights	Read-only review and audit access can be provided for authorised oversight roles, supported by immutable logs and report exports.

C.12 Configuration Panel and No-Code Administration

Parameter Type	Administration Method
Contract values and cost lines	Maintained through administrator-managed DocTypes and custom fields so programme-specific commercial parameters can be updated without code changes.
Zone targets and unit payment rates	Configured in dedicated parameter records with permission-controlled forms and audit logging.
Milestone structures and tranche percentages	Managed through project templates, milestone definitions, and configuration records for approval and payment logic.
Organisational role names and approval tiers	Mapped through role configuration, workflow definitions, and RBAC rules maintained by Tier 1 administrators.
Workflow stages and notification rules	Configured through Frappe workflow and alert configuration tools rather than source-code edits.
Report definitions and operational views	Managed through report builder, print format, and dashboard configuration, with deeper changes handled only where custom logic is required.

C.13 System Architecture Design

1. User Layer

Programme actors interacting with the platform at different control levels.

Executive and Admin Control

- System administrators and PMO leads
- Configuration Panel ownership
- Financial, governance, and HR oversight

Operational Users

- Contract, programme, vendor, and HR users
- Restricted workflows and dashboard access
- Role-based approval and data-entry permissions

2. Capture & Workflow Layer

Operational forms, submissions, approvals, and import channels.

Programme Transactions

- Milestones, claims, contracts, meetings, HR records
- Mandatory fields and attachment gates
- Approval-driven status transitions

FDT Integration

- CSV batch imports and validation
- Deduplication and discrepancy handling
- Immutable import event records

3. Core Platform Layer

ERPNext/Frappe services for data, business logic, and governance controls.

AIPMS Core

- Milestone, contract, payment, document, governance, reporting, and HR modules
- Configuration-driven master data and programme parameters

Control Engine

- RBAC, approvals, alerts, and escalation routing
- Retention, payment certification, and reconciliation logic

4. Integration Layer

External interfaces and technical services connected to AIPMS.

External Inputs

- FDT batch files and optional API integration
- Email notifications and export delivery channels

Infrastructure Services

- Database, backups, audit logging, and storage
- Security, encryption, and monitoring

5. Output & Oversight Layer

Decision support, auditability, and management visibility.

Operational Intelligence

- Governance, PMO, finance, HR, escalation, and import log dashboards
- Role-appropriate reporting and export outputs

Audit & Compliance

- Immutable logs, document history, and approved-record control
- Read-only audit access and transition-ready exports

End-to-End Process Flow

Programme Parameters Configured

→

Operational Records and FDT Data Captured

→

Workflow, Validation, and Approval Controls Applied

→

Dashboards, Certificates, Reports, and Audit Outputs Generated

CI/CD and Disaster Recovery Flow

Focused schematic showing how approved releases move through staging into production, and how the same controlled pipeline supports rollback and disaster-recovery rebuild to a known release state.

1. SOURCE

Version-Controlled Release

Approved source and release tag

- Custom app code and configuration changes committed to source control
- Approved release package tagged for deployment

2. VALIDATE

CI Build and Test

Automated quality gate before release

- Automated build, packaging, and quality checks
- Staging deployment for verification before production release

3. RELEASE

Production Deployment

Controlled promotion into live service

- Controlled promotion of approved release to production
- Monitoring, smoke tests, and release confirmation

4. RECOVER

Rollback or DR Rebuild

Return to known approved state

- Restore database and storage from backup set
- Redeploy approved application release through the same pipeline

BACKUP

Protected Recovery Data

Backup set and PITR readiness

- Nightly encrypted backups and point-in-time recovery logs
- Secondary backup copy and restore verification

CONTROL

Change and Release Governance

Approved promotion and rollback control

- Approved release state documented for production
- Rollback path maintained for failed deployments

OUTCOME

Operational Continuity

Recovered environment resumes service

- Recovered environment returns to a known approved version
- Application, data, and support runbook restored together

Section D: Project Plan & Delivery Timeline

Post-Installation Support Snapshot

Hypercare: 4 weeks immediately after go-live (Weeks 9-12) covering rapid incident response, production tuning, reporting refinements, and user support.

Year 1 Support Retainer: 12 months after formal handover covering bug fixes, security patching, SLA support, backup and monitoring review, and agreed minor enhancement hours.

Renewal Options: optional Year 2 and Year 3 retained support under the commercial schedule.

Programme Timeline Graph

Visual summary of the phased AIPMS delivery plan from mobilisation through full go-live, hypercare, and final handover.

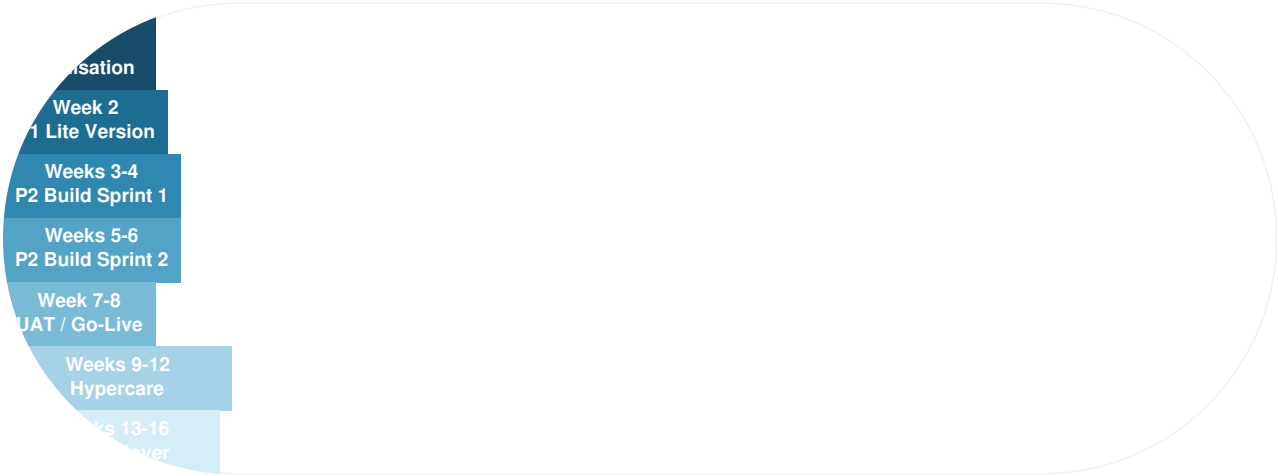

Week 1
Kick-off, hosting, users, parameters, and mobilisation plan.

Week 2
Modules 1-5 live for programme commencement.

Weeks 3-4
Dashboards, HR/payroll setup, FDT import development.

Weeks 5-6
Integration testing, payroll parallel runs, exports, and hardening.

Week 7-8
UAT closure, security review, production cutover, and training completion.

Weeks 9-12
Hypercare support, tuning, and issue resolution.

Weeks 13-16
Final documentation, knowledge transfer, and support transition.

Committed delivery profile: Lite Version by end of Week 2, Full Configuration complete by end of Week 6, UAT and hardening in Week 7, Full Go-Live by end of Week 8, followed by four weeks of hypercare and structured handover through Week 16.

W1

P0P1P2 BuildConfig/UATGo-LiveHypercare + Handover

Week	Phase	Activities	Deliverables / Acceptance Gate
Week 1	P0 Mobilisation	Kick-off, confirmation of stakeholders, environment setup, parameter workshops, user/role setup, draft backlog confirmation	Hosting active, user access tested, configuration plan approved
Week 2	P1 Lite Version	Core delivery of Modules 1-5, initial RBAC, key document templates, meeting workflow, contract register activation, WCA setup, and baseline payment workflow configuration	Lite Version accepted for programme commencement
Weeks 3-4	P2 Build Sprint 1	Module 6 dashboard build, Module 7 HR/payroll configuration, statutory deduction setup, FDT CSV import development, salary structure templates, and bulk onboarding tools	Configured Modules 3, 6, and 7 ready for integrated review
Weeks 5-6	P2 Build Sprint 2	End-to-end FDT testing, payment certificate linkage, offline attendance testing, payroll parallel runs, refined exports, security hardening, training materials, and test-script completion	Full configuration completed and ready for UAT sign-off
Week 7	UAT & Security	UAT defect resolution, penetration testing, remediation of critical findings, final training material packaging, and go-live readiness review	UAT sign-off, critical findings resolved, go-live approved
Week 8	P3 Full Go-Live	Production cutover, first live FDT import, first payroll cycle validation, Tier 1-7 training completion, and operational transition to live service	All seven modules live in production
Weeks 9-12	Hypercare	Named support lead, rapid issue response, production tuning, reporting refinements, usage support	Hypercare SLA active with weekly issue review
Weeks 13-16	P4 Handover	Final documentation, admin knowledge transfer, support transition, enhancement backlog definition, service reporting cadence	P4 handover complete and Year 1 support retainer active

D.1 Phase-by-Phase Delivery Detail

Phase	Detailed Scope	Acceptance Signal

Phase	Detailed Scope	Acceptance Signal
P0 Mobilisation	Contract execution, kick-off, hosting provisioning, parameter loading into the Configuration Panel, user creation, and P1 configuration plan submission.	Hosting active, parameters confirmed, user access tested.
P1 Lite Version	Modules 1-5 operational at core level: milestone scheduling, contract register, SVR workflow, WCA and claim workflow, document repository, meeting calendar, minutes, and baseline RBAC.	Written Lite Version sign-off by end of Week 2.
P2 Full Configuration	Dashboards and reports, HR/payroll engine, statutory deduction setup, bulk onboarding, FDT CSV import, integration testing, and structured UAT support.	Configured system ready for full UAT and operational review.
P3 Full Go-Live	Production go-live, live FDT processing, first payroll run, training completion, and start of hypercare support.	Production acceptance by end of Week 8.
P4 Handover	Technical documentation, user documentation, knowledge transfer, closure reporting, and transition into support retainer operations.	Final handover accepted and support cadence active.

Section D Supplement: Post-Installation Support Model

Inspired Delta Ltd proposes a two-stage post-installation support model for AIPMS. The first stage is a structured **hypercare period covering Weeks 9-12** immediately after production go-live. During this period, a named support lead will manage rapid issue response, production tuning, reporting refinements, user support, and daily or weekly issue review with the client team depending on incident volume and operational criticality.

The second stage is a **12-month Year 1 support retainer** commencing after formal handover. This retained support period is intended to cover bug fixes, security patches, SLA-based incident support, backup and monitoring review, and an agreed allowance for minor monthly enhancement effort. Support operations will follow a documented service cadence with issue logging, resolution tracking, and periodic service reporting to authorised AIPMS stakeholders.

At the close of the handover phase, Inspired Delta Ltd will deliver the technical documentation, user guidance, administrative knowledge transfer, and enhancement backlog needed to transition the platform into steady-state support. Optional Year 2 and Year 3 support renewals remain available under the commercial schedule.

Support Stage	Period	Support Focus
Hypercare	Weeks 9-12 after go-live	Rapid incident response, production tuning, user support, reporting refinements, and go-live stabilisation.
Year 1 Support Retainer	12 months post handover	Bug fixes, security patching, SLA support, monitoring and backup review, and agreed minor enhancement hours.
Optional Renewal Support	Year 2 and Year 3	Continued retained support under renewal pricing as stated in the commercial schedule.

D.2 Team Structure

Role	Assigned Lead	Proposal Note
Project Manager	Taiwo Eugene Akinosho	Overall delivery governance, mobilisation, stakeholder coordination
Lead Solutions Architect	Lucky Okpuno	Solution design, module fit, platform architecture, commercial scoping
Lead Developer	TK Emiko	Custom Frappe app development, workflow, integration, and reporting components
QA Lead	Rose Soyinka	Test planning, UAT coordination, acceptance readiness

Role	Assigned Lead	Proposal Note
HR & Payroll Specialist	[Insert name before final submission]	Payroll rules, statutory deductions, HR controls, training
DevOps / Hosting Lead	Ayo Damola Ogunleye	Infrastructure, backup, monitoring, deployment hardening

Appendix required before submission: CVs for all named key personnel and any delivery partner resources.

D.3 Top Delivery Risks and Mitigations

Risk	Impact	Mitigation
Delay in receiving approved programme parameters or user lists	Mobilisation slippage and delayed Lite acceptance	Run a structured Week 1 data workshop, use signed parameter templates, and escalate missing decisions within 24 hours
Late or unstable FDT schema/sample data	Delay to payment automation and end-to-end validation	Build using a versioned import schema, validate against sample batches early, and isolate discrepancies in import logs
Complex payroll edge cases discovered during configuration	Errors in remuneration or statutory deductions	Conduct parallel payroll testing before go-live and secure HR sign-off on rule configuration before production use
Stakeholder availability for UAT and approval workflows	Acceptance delay despite technical readiness	Publish UAT calendar in Week 2, assign named approvers, and track unresolved issues daily during Week 7
Security or performance issue in custom components	Go-live risk or remediation effort	Use peer review, staged deployment, pre-go-live testing, and penetration testing before production sign-off

Section E: Commercial Proposal

All prices below are planning estimates stated in Nigerian Naira (₦) using a working conversion rate of **₦1,400 per US$1**. VAT treatment should be confirmed in the final commercial submission. These figures are suitable for internal budgeting and draft submission shaping, but should be approved commercially before issue.

E.1 Fixed-Price Delivery Breakdown

Phase / Scope	Description	Price (₦)
P0 Mobilisation	Hosting setup, parameter workshops, role setup, configuration planning	₦8,400,000
P1 Lite Version	Modules 1-5 core functionality, workflows, templates, and initial training	₦25,200,000
P2 Full Configuration	Modules 3, 6, and 7 completion, FDT CSV integration, dashboards, HR/payroll, exports	₦33,600,000
P3 Full Go-Live	UAT support, go-live execution, training completion, production cutover support	₦12,600,000
P4 Handover	Documentation, knowledge transfer, final acceptance support	₦4,200,000
Total Fixed Delivery Fee		**₦84,000,000**

E.2 Hosting, Support, and 3-Year Cost Structure

Item	Description	Monthly Fee (₦)	Annual Fee (₦)
Hosting	Production hosting, backups, monitoring, and maintenance window management	₦1,400,000	₦16,800,000
Year 1 Support Retainer	Bug fixes, security patches, SLA support, and agreed monthly enhancement hours	₦3,500,000	₦42,000,000

Item	Description	Monthly Fee (₦)	Annual Fee (₦)
Year 2 Support Option	Indicative renewal pricing	₦3,150,000	₦37,800,000
Year 3 Support Option	Indicative renewal pricing	₦2,940,000	₦35,280,000

E.3 Training and Optional Enhancements

Item	Description	Price (₦)
Training	Tier 1-7 training programme, user guides, and recorded walkthroughs	Included in fixed delivery fee
Phase 2 API Integration	Scheduled/API-based FDT integration beyond mandatory CSV import	₦11,200,000
AI-Assisted Report Analysis	Configurable multi-engine analysis layer for selected dashboards and management reports, with prompt templates, follow-up review, and controlled user access	₦9,800,000
Mobile HR Check-In	Enhanced field check-in workflow with device/location controls	₦8,400,000
Advanced Gantt / Portfolio View	Enhanced programme schedule visualisation	₦5,600,000

Total 3-Year Cost of Ownership: ₦215,880,000

Price validity: Minimum 90 days from proposal submission date.

E.4 Proposed Payment Terms

Milestone	Trigger	% of Delivery Fee
P0 Mobilisation	Contract execution and mobilisation completion	10%
P1 Lite Version Acceptance	Written sign-off for Modules 1-5 core readiness	25%
P2 Full Configuration Acceptance	Configured Modules 6 and 7, FDT integration, and UAT readiness	35%
P3 Full Go-Live	Production go-live and completion of operational readiness activities	20%
P4 Final Handover	Documentation, handover, and close-out acceptance	10%

Section F: Compliance Declarations

Conflict of Interest: Inspired Delta Ltd declares that, to the best of its knowledge, it has no conflict of interest with Inspired Global Systems Ltd or any party involved in the programme.

Data Protection: Inspired Delta Ltd accepts the requirement to comply with applicable data protection legislation and to execute an appropriate Data Processing Agreement for personal and HR data.

Data Ownership and Exit: Inspired Delta Ltd accepts the data ownership and exit provisions in Section 4.6 of the RFP. Final platform continuity and escrow/open-platform provisions will be documented in the final contract schedule according to the agreed delivery model.

Service Levels: Inspired Delta Ltd accepts the minimum service level requirements in Section 5, including uptime, response targets, backup verification, and support-retainer expectations.

Timeline Commitment: Inspired Delta Ltd confirms a Lite Version commitment date of end of Week 2 and a Full Go-Live commitment date of end of Week 8, both within the RFP maximum timetable.

Exceptions: No exceptions are declared in this draft proposal. Any commercial, legal, or hosting-schedule clarifications should be disclosed explicitly in the final PDF submission if required.

Submission Checklist for Final PDF

Required Finalisation Item	Status in This Draft	Action Before Submission
Registered address, CAC number, bid contact	**Pending**	Insert corporate details
Three complete client references with values, dates, and verification contacts	**Pending**	Complete Section B appendix
Detailed Annex A compliance matrix	**Pending**	Attach final line-by-line matrix
CVs for key personnel	**Pending**	Attach appendix
Named HR specialist and DevOps lead	**Pending**	Replace placeholders
Commercial figures and VAT statement	**Pending**	Insert approved pricing
Declared hosting/data residency location	**Pending**	Confirm final production hosting schedule
